



Finance & Audit Committee

CENTRAL VALLEY STATUS REPORT

March 2023 Report (data through January 2023)

Executive Summary

Construction Packages (CP) Design-Build Expenditures ([Page 5](#))

- January 2023 Expenditures totaled \$50.5M:
 - Construction Package 1 (Page 14) - Expenditures totaled \$14.3M.
 - Construction Package 2-3 (Page 23) - Expenditures totaled \$31.9M.
 - Construction Package 4 (Page 34) - Expenditures totaled \$4.2M.
- Total CP Cumulative Actual Expenditures (Pages 13, 22, and 31) – \$4,435.6M.
- Total Cumulative Current Contract Amount (Pages 13, 22, and 31) – \$6,710.1M.

Change Orders

- Executed Change Orders this period – 13 for a total of \$86.1M:
 - Construction Package 1 (Page 15) – Six for a total of \$79.4M.
 - Construction Package 2-3 (Page 24) – Four for a total of \$5.0M
 - Construction Package 4 (Page 35) – Three for a total of \$1.7M.

Risk Contingency ([Page 6](#))

- Approved Contingency – \$4,000.7M budgeted contract contingency. Contingency balance is \$271.2M as of January 31, 2023.
 - Construction Package 1 (Page 16) – \$1,944.5M budgeted contract contingency. Contingency balance is \$170.3M as of data date.
 - Construction Package 2-3 (Page 25) – \$1,638.4M budgeted contract contingency. Contingency balance is \$56.3M as of data date.
 - Construction Package 4 (Page 36) – \$417.8M budgeted contract contingency. Contingency balance is \$44.6M as of data date.

CP Design (Structures/Guideway)

- CP major design - Ready for Construction (RFC). Milestone of 100% of the required 163 RFC design approvals agreed with the Authority in June 2022 for Construction.
 - Construction Package 1 – 40 of 40 total design packages approved by the Authority for construction.
 - Construction Package 2-3 – 109 of 109 total design packages approved by the Authority for construction.
 - Construction Package 4 – 14 of 14 total design packages approved by the Authority for construction.

CP Construction Labor ([Page 7](#))

- January 2023, Average Daily Site Workers (by Week) (Page 7) – 874 workers. A decrease of 90 workers from the previous period (from 964):
 - Construction Package 1 (Page 17) – 192 workers. A decrease of 59 workers from the previous month (251).
 - Construction Package 2-3 (Page 26) – 518 workers. A decrease of 31 workers from the previous month (549).
 - Construction Package 4 (Page 37) – 164 workers. No change in workers from the previous month (164).
- Contractors continued with construction while following safety protocols and guidelines from the Centers for Disease Control and Prevention (CDC) and Occupational Safety and Health Administration (OSHA).

CP Construction Progress (Page 8)

- Structures – 69 underway/construction complete compared to 93 structures (74%) total. No change from the previous period.
 - Construction Package 1 – 26 structures underway/construction complete.
 - Construction Package 2-3 – 32 structures underway/construction complete.
 - Construction Package 4 – 11 structures underway/construction complete.
- Guideway – 88 miles underway/construction complete compared to 119 miles (74%) total. No change from the previous period.
 - Construction Package 1 – 18 miles underway/construction complete.
 - Construction Package 2-3 – 48 miles underway/construction complete.
 - Construction Package 4 – 22 miles underway/construction complete.

Utility Relocations Status (Page 9)

- Relocated: 978 (53%); In Progress: 388 (21%); Approved to Start: 16 (1%); Not Started: 454 (25%); Total: 1,836. A total of one relocated in January 2023. A sequence of activities must be completed to begin utility relocation work. These activities include environmental clearance, executed third-party agreement(s), design approval, construction work plans, pre-construction walkthroughs, acquisition of real property, and/or land right conveyances:
 - Construction Package 1 – Relocated: 458 (46%); In Progress: 311 (31%); Approved to Start: 0 (0%); Not Started: 223 (23%); Total: 992.
 - Construction Package 2-3 – Relocated: 422 (60%); In Progress: 59 (8%); Approved to Start: 0 (0%); Not Started: 220 (31%); Total: 701.
 - Construction Package 4 – Relocated: 98 (69%); In Progress: 18 (13%); Approved to Start: 16 (11%); Not Started: 11 (7%); Total: 143.

CP Real Property/Right-of-Way (ROW) (Pages 10 - 12)

- Total Parcels Delivered to Date – 2,213 parcels compared to an estimated 2,299 parcels needed.
- Parcels Delivered to Design-Builder (DB) – Five parcels in January 2023.
- Construction Packages 1-4 – Zero parcels added, and one parcel removed. The Authority continues to receive requests for additional parcels primarily related to third-party requirements. The Authority reviews these as received and if merit is found, those parcels will be added and acquired per contractual terms.
- Railroad Parcels Delivered to Design-Builder – Six parcels.
- Total Railroad Parcels Delivered to Date – 143 parcels delivered compared to an estimated 170 total railroad parcels needed.
- Land Right Conveyances (Tier 1, Prior to Construction):
 - Zero land right conveyances approved.
 - To date, the Authority received approval on 667 land right conveyances.

Project Development (Environmental Clearance) Schedule – Notice of Determination (NOD)/Record of Decision (ROD) ([Pages 42 - 43](#))


- San Francisco to San Jose – Work through NOD/ROD has been completed. Staff continues to assemble the Administrative Record.
- San Jose to Merced – Work through NOD/ROD has been completed. Staff continues to assemble the Administrative Record.
- Bakersfield to Palmdale – Work through NOD/ROD has been completed. Continued meeting with key stakeholders, including the Center for Biological Diversity.
- Palmdale to Burbank – The Draft Environmental Impact Report/Environmental Impact Statement (EIR/EIS) was released to the public on September 2, 2022. The public comment period was extended from 60 days to 90 days and closed on December 1, 2022. Continued to coordinate with the Regional Consultant to prepare responses to comments received on the Draft EIR/EIS.
- Burbank to Los Angeles – Work through NOD/ROD has been completed. Project closeout activities are ongoing.
- Los Angeles to Anaheim – Continued integrating additional Burlington Northern Santa Fe Corporation (BNSF) deliverables pertaining to the Colton and Lenwood facilities into the assembled Administrative Draft EIR/EIS.

Project Development (Post-Record of Decision) Schedule ([Page 44](#))

- Merced Extension (Merced to Madera) – Stantec Inc., under Agreement HSR 22-02, continues to make progress on the early actions of this Project, including submittal of various draft documents such as the Project Management Plan-Draft.
- Fresno to Bakersfield Locally Generated Alternative (LGA) – HNTB Corporation (HNTB), under agreement HSR 22-01, continues to make progress on the early actions of this Project, including submittal of various draft documents such as the Project Management Plan and the BNSF Shoofly Alignment - Draft.

CP 1-4 – Design-Build Expenditures

CP 1-4 – Monthly Expenditures (\$ Millions)

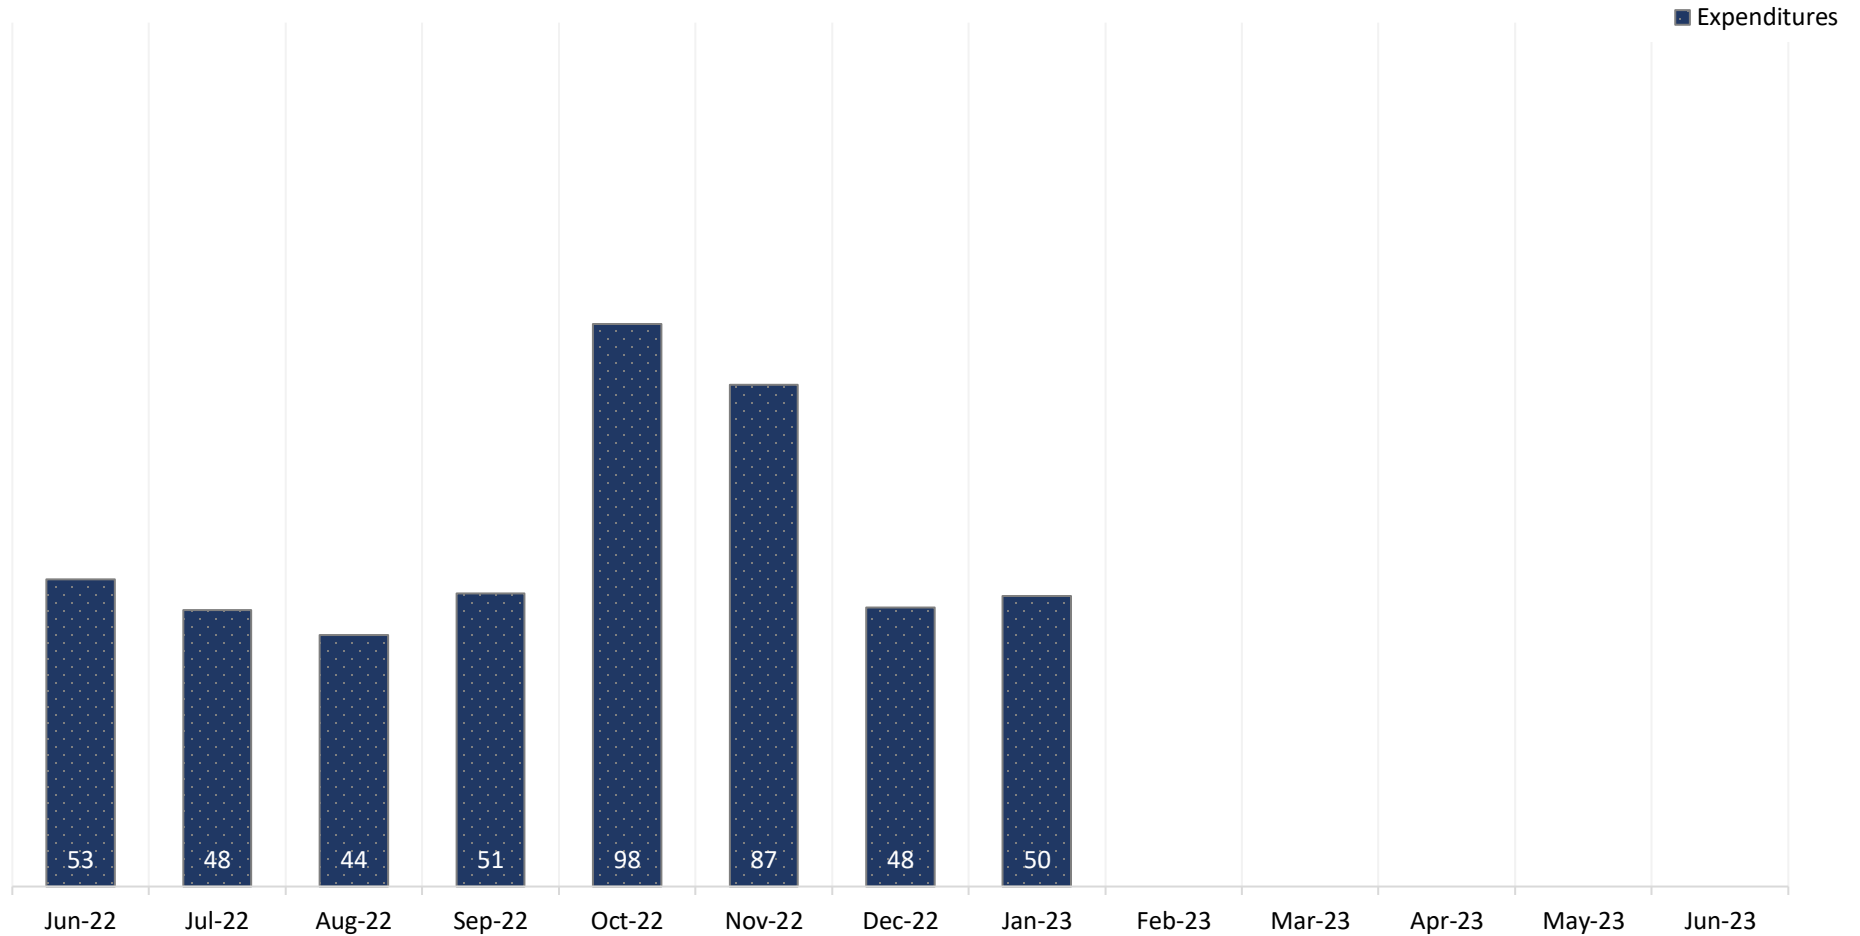


Notes:

1. Expenditures in the chart above are specific to the Design-Builder production and based on the Capital Outlay and Expenditure Report.
2. January 2023 Expenditures totaled \$50.5M:
 - a. Construction Package 1 – Expenditures totaled \$14.3M.
 - b. Construction Package 2-3 – Expenditures totaled \$31.9M.
 - c. Construction Package 4 – Expenditures totaled \$4.2M.

CP 1-4 – Risk Contingency

CP 1-4 – Risk Contingency Status (\$ Millions)

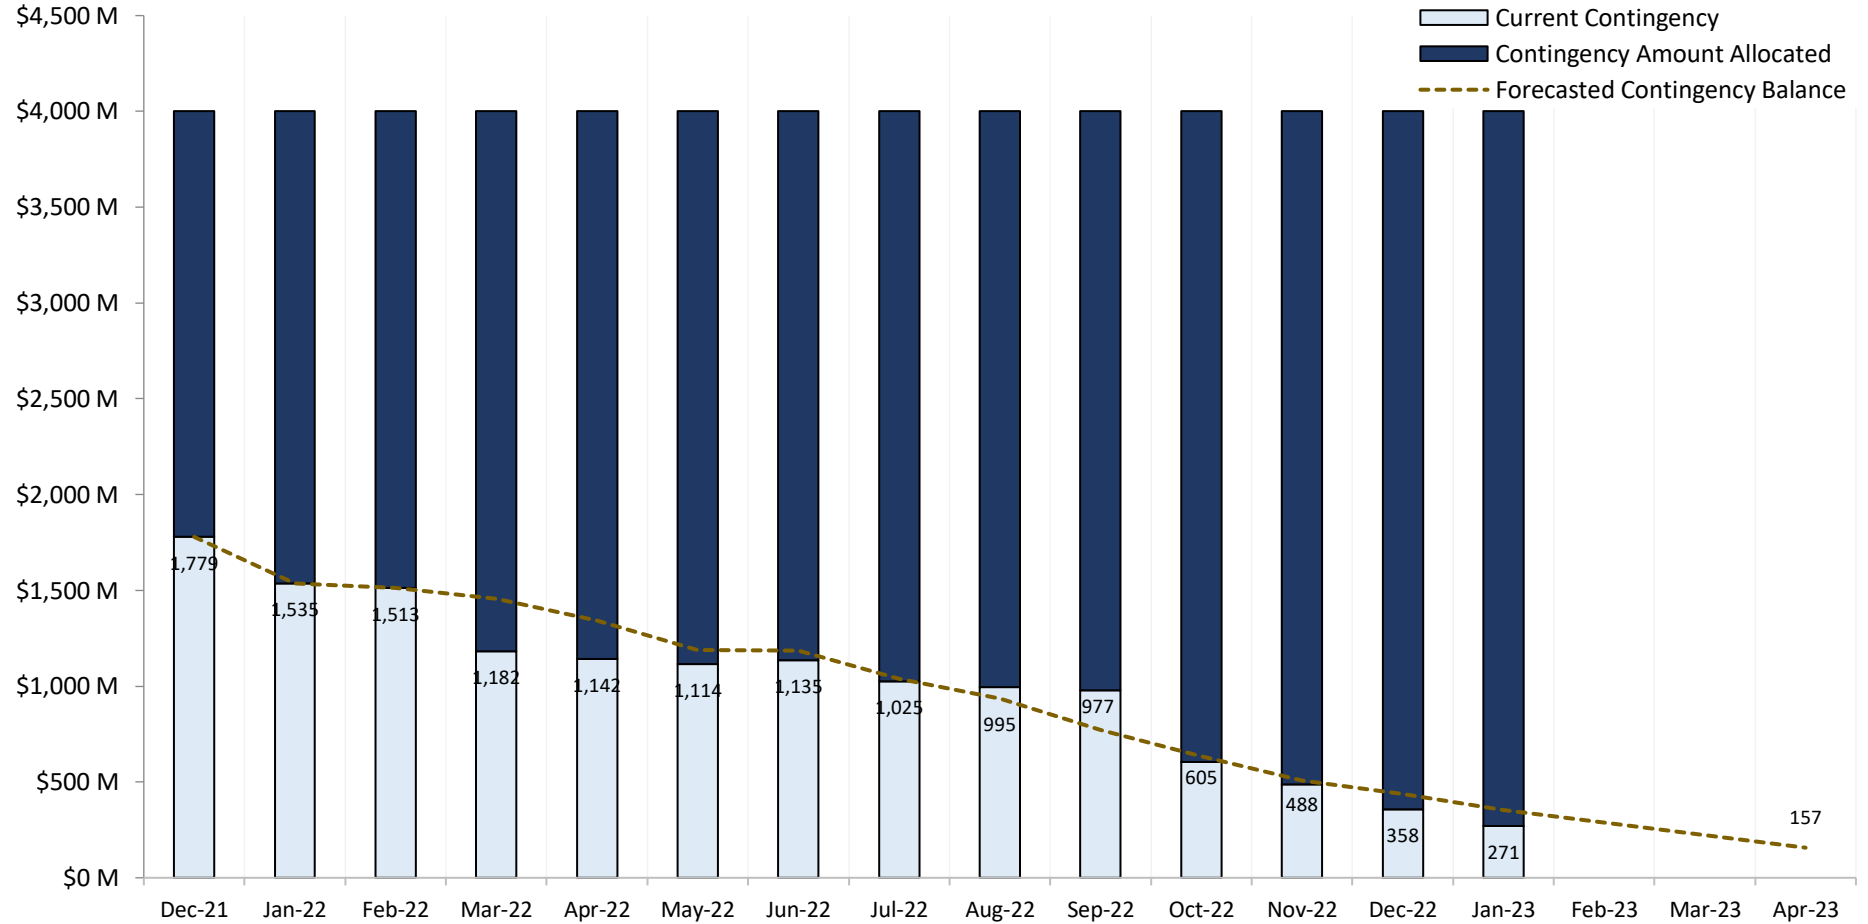


Notes:

1. Program baseline is \$4,000.7M.
2. Contingency balance updated to reflect the Board’s adoption of Resolution #HSR21-11 (Expenditure Authorization Increase).
3. Contingency Amount Allocated reflects all executed change orders and Business Oversight Committee (BOC) approved items for all CPs.
4. The Forecasted Contingency Balance drawdown curve is based only on agreed change orders expected to be executed within the three-month window. Due to change order negotiations, and dispute resolution, timing and value of Forecasted Contingency Balance is uncertain.

CP 1-4 – Construction Labor

CP 1-4 – Monthly Construction Workforce Total – Actual (FTE)

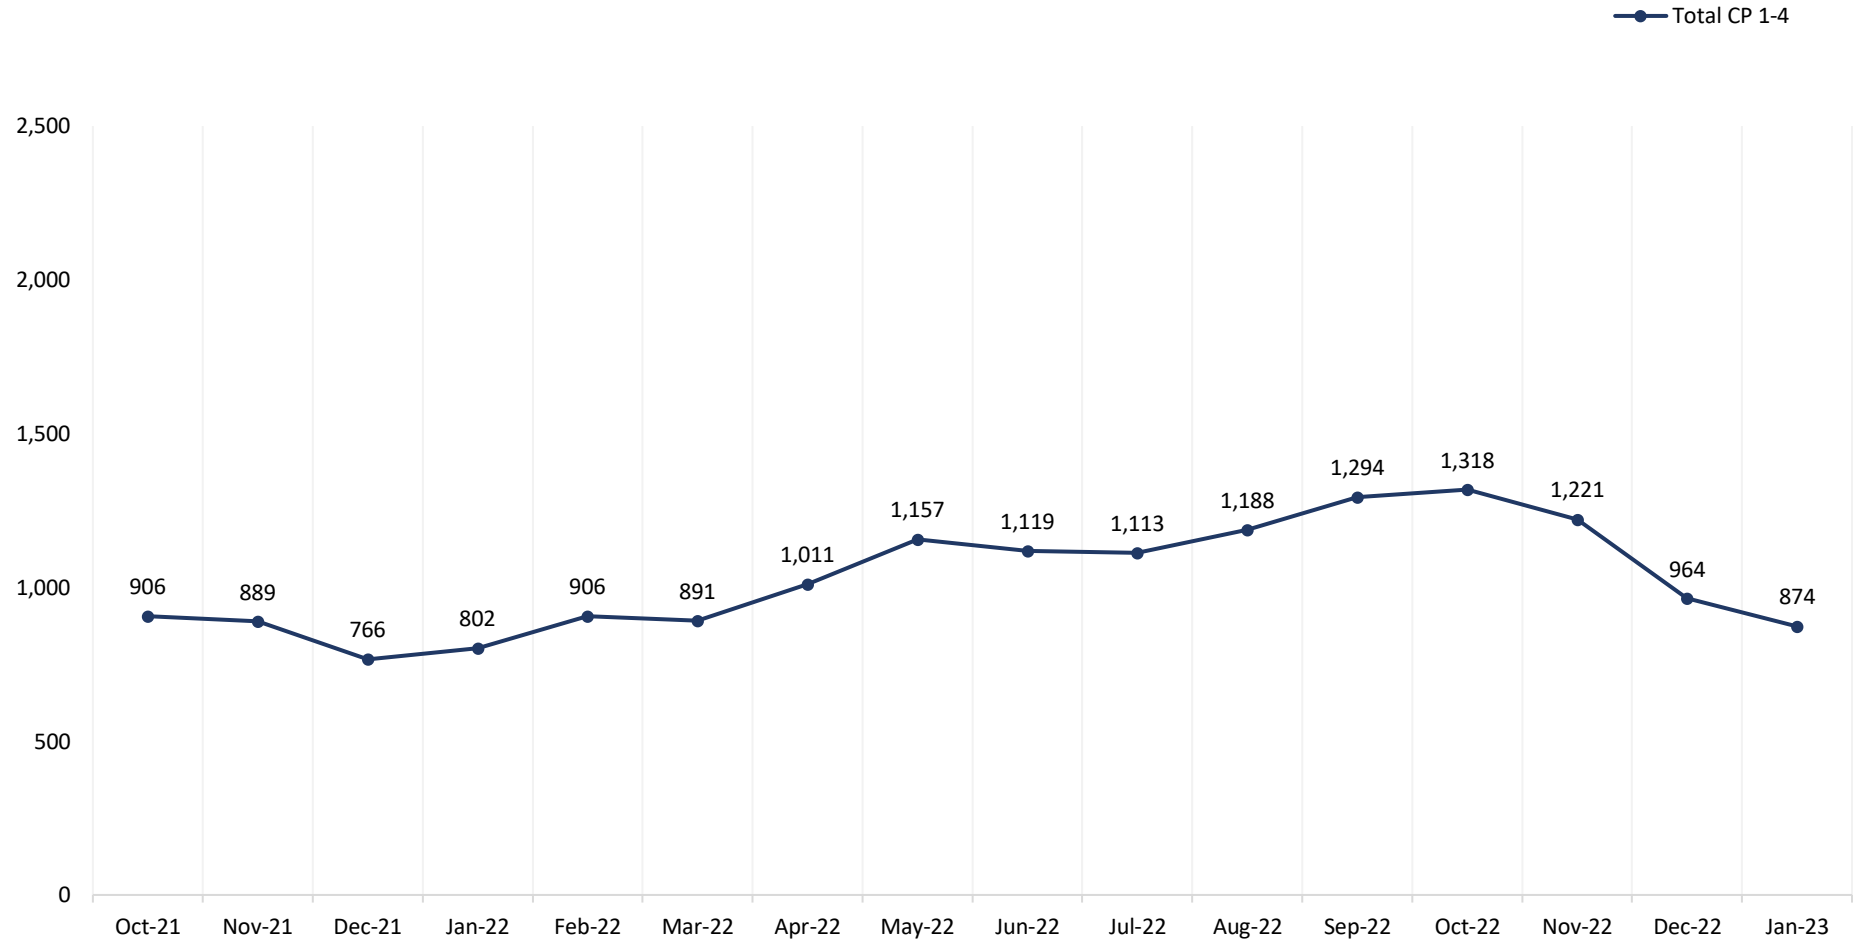


Notes:

1. The construction labor numbers (full-time employees) are based on the weekly totals divided by the number of weeks within the working calendar month and represents the Average Daily Site Workers (by week).
2. January 2023, Average Daily Site Workers (by week) – 874 workers. A decrease of 90 workers from the previous period (from 964): Decrease in labor numbers due to multiple rain events.
 - a. Construction Package 1 (Page 17) – 192 workers. A decrease of 59 workers from the previous month (251).
 - b. Construction Package 2-3 (Page 26) – 518 workers. A decrease of 31 workers from the previous month (549).
 - c. Construction Package 4 (Page 37) – 164 workers. No change in the number of workers from the previous month (164).

CP 1-4 – Construction Progress

CP 1-4 – Construction Progress to Completion – Forecast vs. Actual

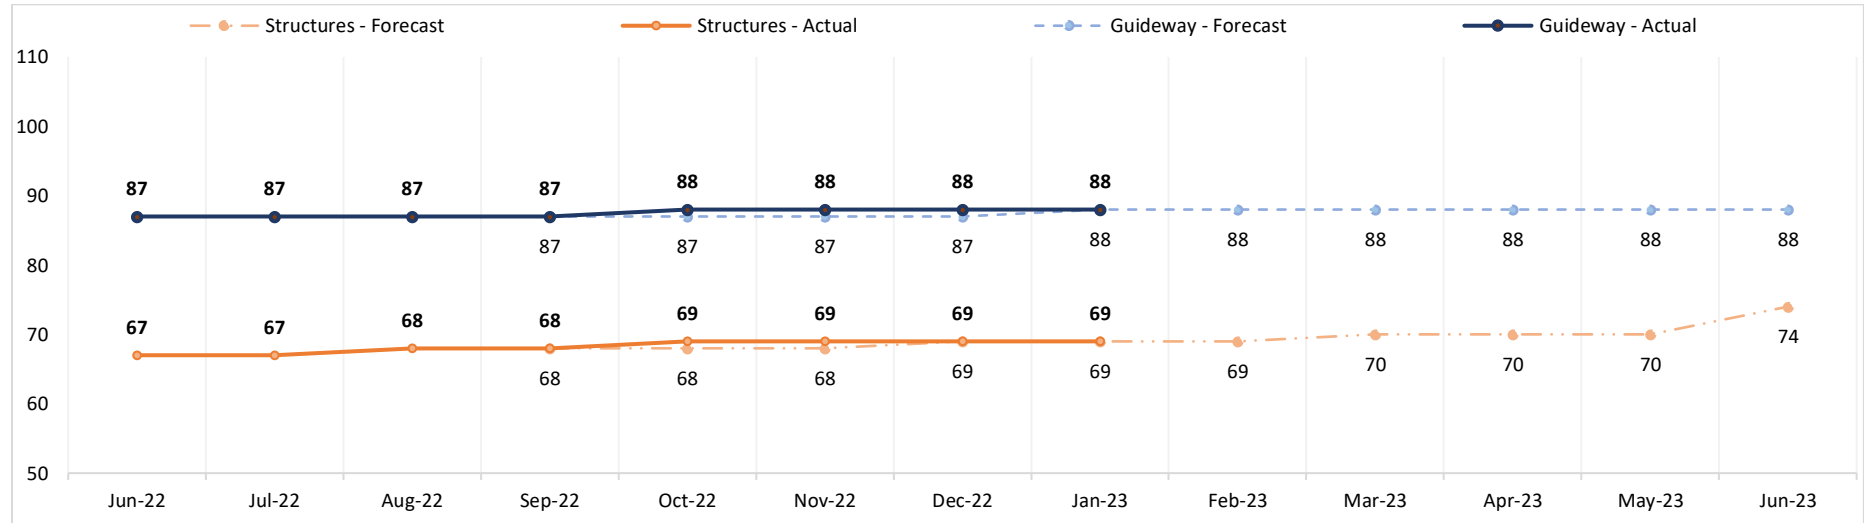

Monthly Construction Status – In Progress vs. Completed

Construction	CP 1		CP 2-3		CP 4		Overall		Total
	In Progress	Completed	In Progress	Completed	In Progress	Completed	In Progress	Completed	
Structures	10	16	18	14	5	6	33	36	69
Guideway	16	2	15	33	8	14	39	49	88

Notes:


1. The chart above incorporates provisional forecast numbers as of September 2022 pending final approval of Revised Baseline Schedules (RBS) Revision 4 for CP 1 .
2. Construction Complete definition:
 - a. Structure Completion – all concrete work is complete.
 - b. Guideway Completion – earthworks complete with rough grading.
3. Total Structures: 93
4. Structures – 69 underway/construction complete compared to 93 structures total. (74%). No change from the previous period.
 - a. CP 1 – 26 structures underway/construction complete.
 - b. CP 2-3 – 32 structures underway/construction complete.
 - c. CP 4 – 11 structures underway/construction complete.
5. Total Guideway: approximately 119 miles
6. Guideway – 88 miles underway/construction complete compared to 119 miles total. (74%). No change from the previous period.
 - a. CP 1 – 18 miles underway/construction complete.
 - b. CP 2-3 – 48 miles underway/construction complete.
 - c. CP 4 – 22 miles underway/construction complete. The actual miles for CP 4 are 21.5 miles but rounded to 22 miles for consistency in reporting.

CP 1-4 – Utility Relocations

CP 1-4 – Utility Relocation Summary

Construction Package	Total Relocations January 31, 2023	Total Utilities Relocated to Date January 31, 2023	Remaining Utility Relocations January 31, 2023
CP 1	992	458	534
CP 2-3	701	422	279
CP 4	143	98	45
Total	1,836	978	858

CP 1-4 – Utility Relocation Status Summary-Monthly

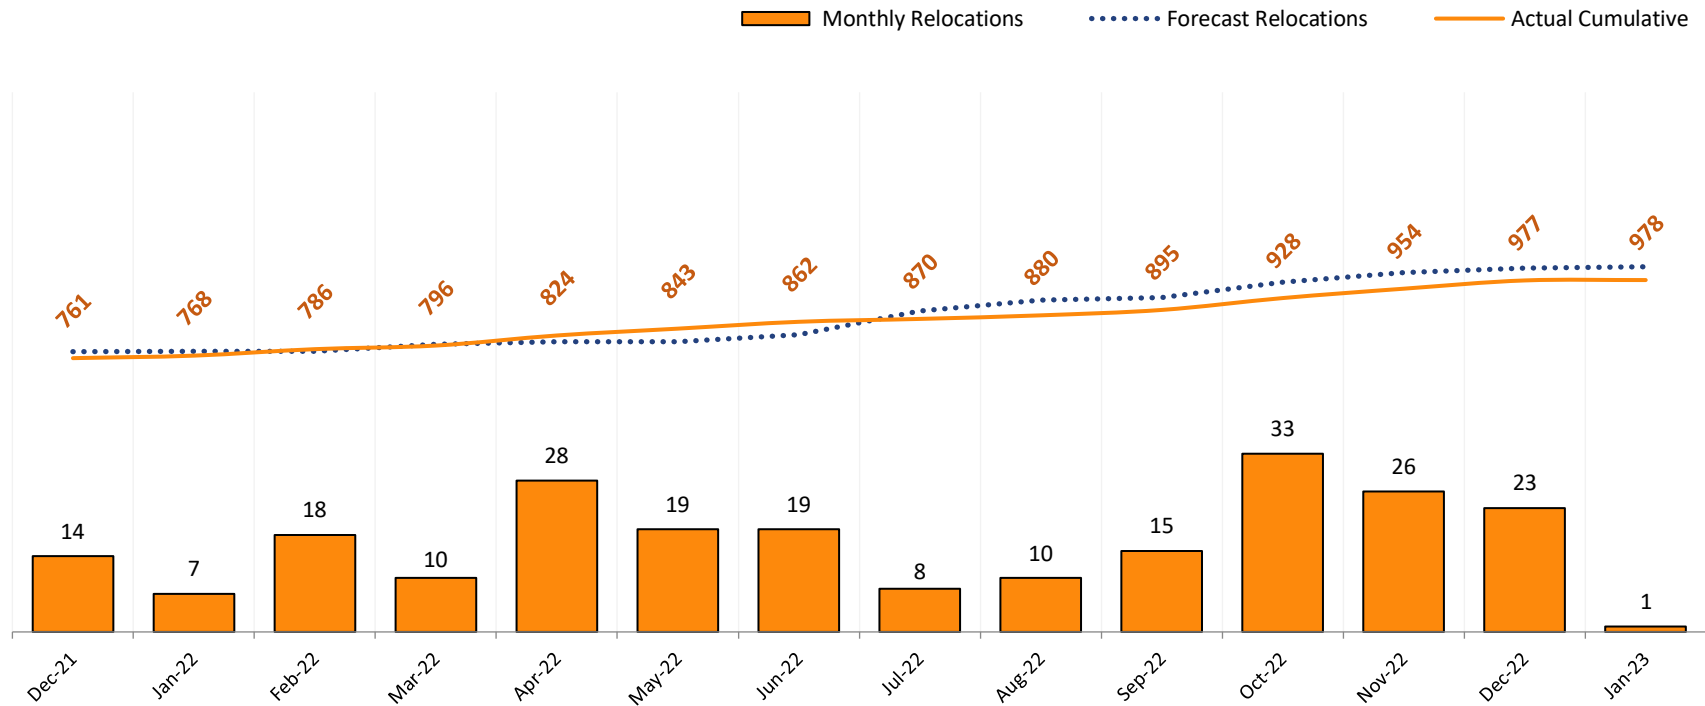

Notes:


1. In Progress 388 (21%).
2. Approved to start 16 (1%).
3. Not Started 454 (25%).

CP 1-4 – Real Property/Right-of-Way (ROW)

CP 1-4 – Right-of-Way (ROW) Summary

Construction Package	Total Needed Parcels January 31, 2023	Total Parcels Delivered to Date January 31, 2023	Remaining Parcels to be Delivered January 31, 2023
CP 1	1,082	1,058	24
CP 2-3	986	935	51
CP 4	231	220	11
Total	2,299	2,213	86

CP 1-4 – Parcel Delivery to Design-Builder (DB) Summary

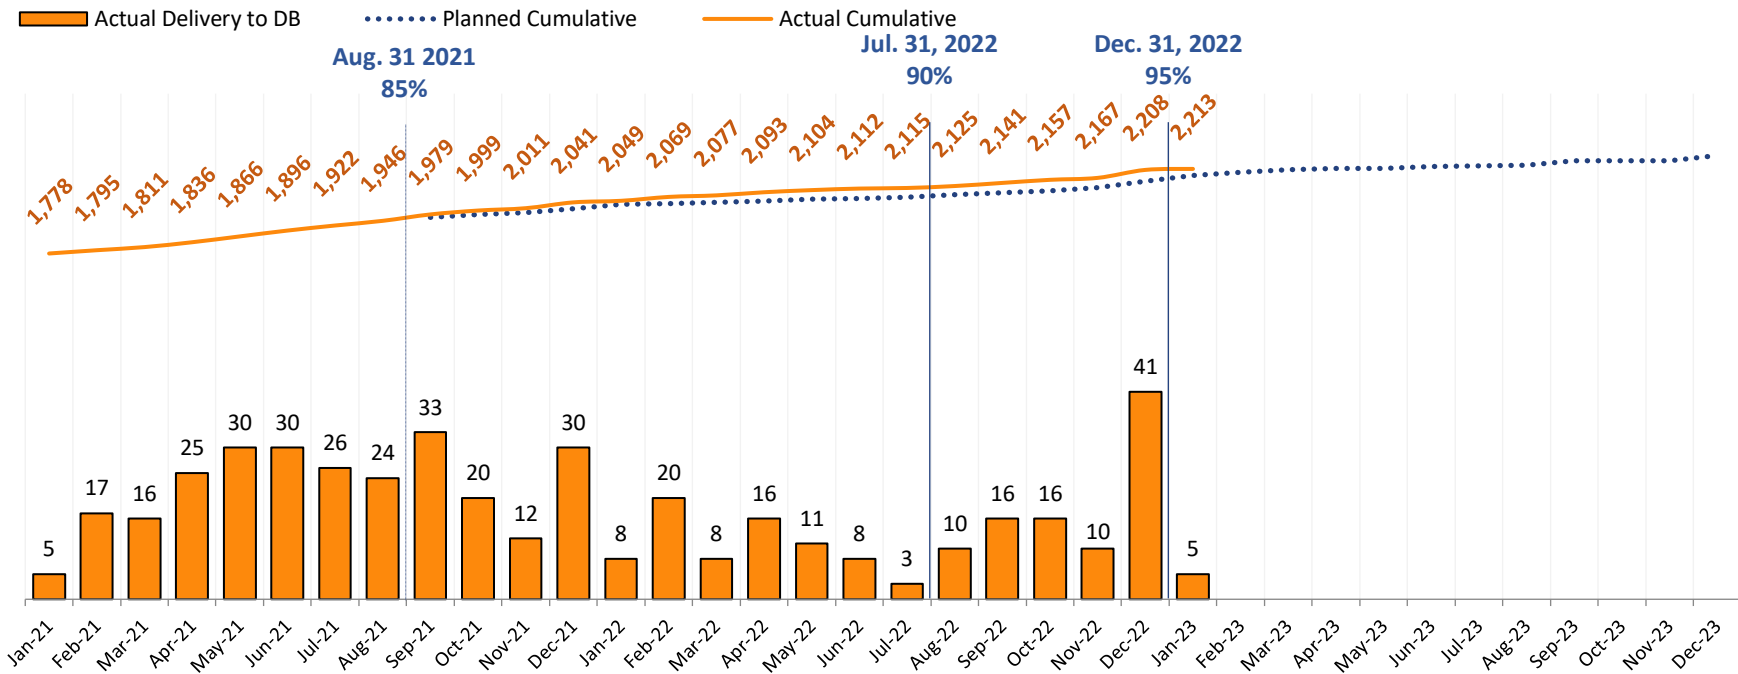

Notes:


1. This reflects the actual parcels delivered to the Design-Builder by month compared to the planned delivery schedule which identifies 90% and 95% milestone completion for CP 1-4.
2. Delivery to Design Builder 90% milestone completion was achieved for CP 1-4 in March 2022.
3. Real Property delivered 41 parcels in December 2022 which brings the total percentage of parcels delivered to 96%, surpassing their goal of 95% by the end of December 2022.
4. Total Parcels Needed was reduced by one parcel.

CP 1-4 – Real Property/Right-of-Way (ROW) Railroad

CP 1-4 – Right-of-Way (ROW) Railroad Summary

Construction Package	Total Needed Railroad Parcels January 31, 2023	Total Railroad Parcels Delivered to Date January 31, 2023	Remaining Railroad Parcels to be Delivered January 31, 2023
CP 1	83	63	20
CP 2-3	58	51	7
CP 4	29	29	0
Total	170	143	27

CP 1-4 – Railroad Parcel Delivery to Design-Builder (DB) Summary

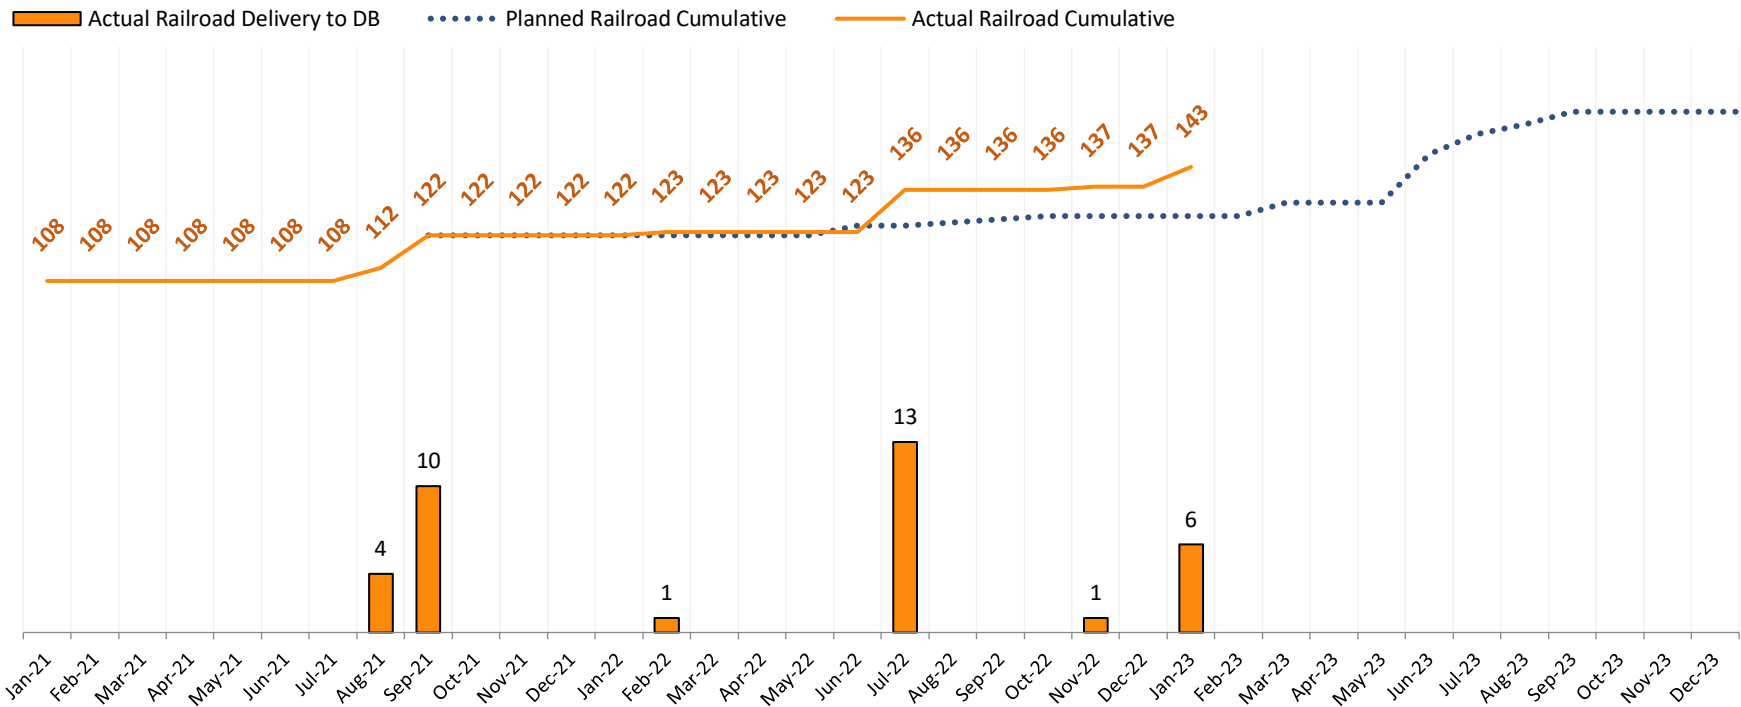

Notes:


1. The Planned Cumulative line for Railroad Parcel Delivery reflects provisional forecasts as of September 2022 pending final approval of Revised Baseline Schedules (RBS) Revision 4 for CP 1.
2. Two Railroad parcel delivery dates are being reforecast, not impacting the critical path.

CP 1-4 – Tier 1 Land Right Conveyances Required Prior to Construction (PG&E, SCE, FID, FMFCD)

CP 1-4 – Tier 1 Land Right Conveyances Required Prior to Construction (PG&E, SCE, FID, FMFCD) Summary

Construction Package	Total Needed Land Right Conveyances January 31, 2023	Total Land Right Conveyances Approved ⁽²⁾ January 31, 2023	Remaining Land Right Conveyances to be Approved January 31, 2023
CP 1	393	344	49
CP 2-3	433	280	153
CP 4	68	43	25
Total	894	667	227

CP 1-4 – Tier 1 Land Right Conveyances Required Prior to Construction (PG&E, SCE, FID, FMFCD) Summary

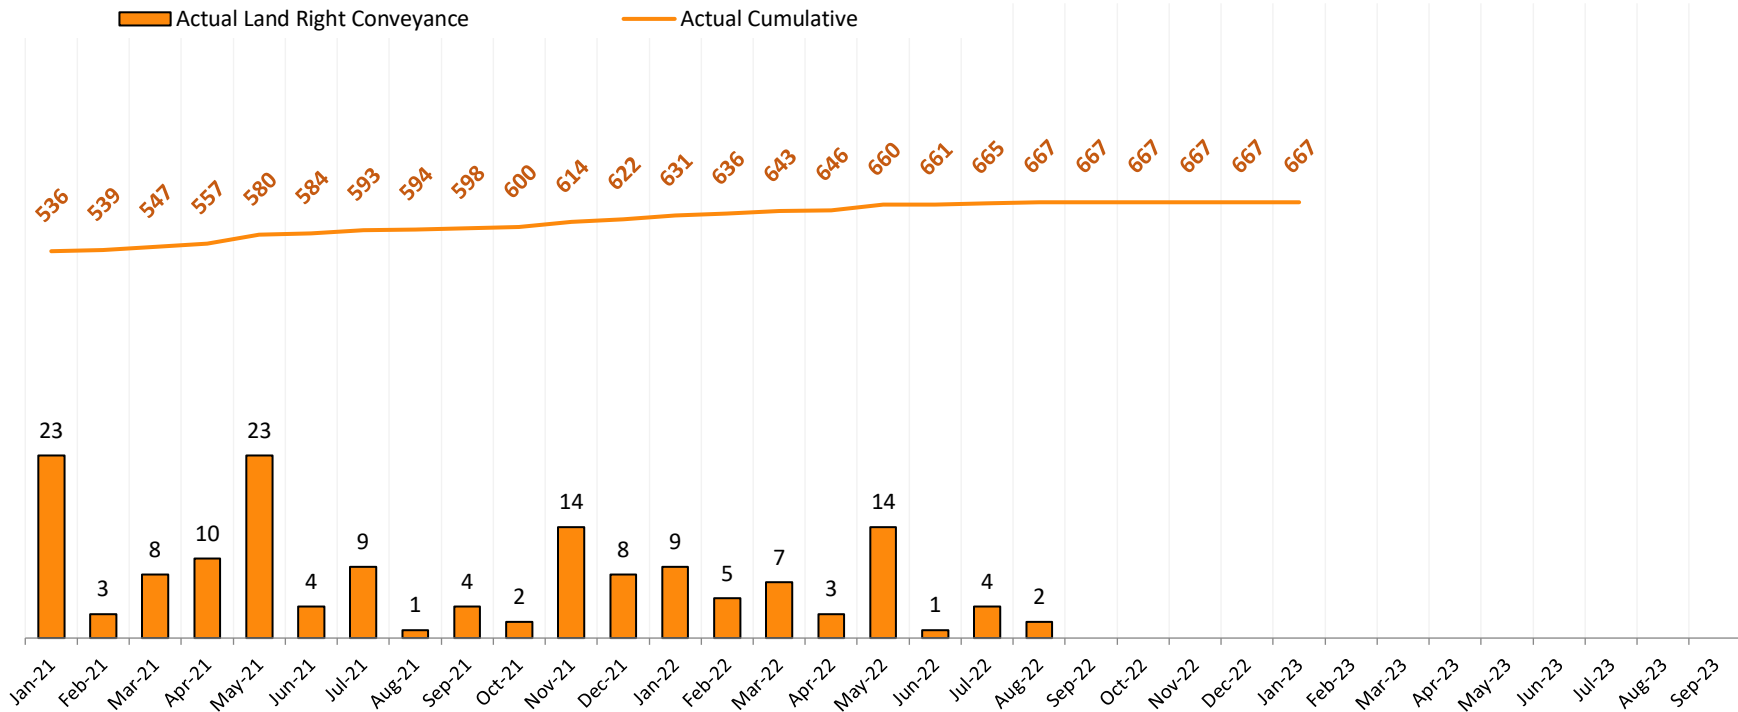

Notes:

1. The Planned Cumulative line for Land Right Conveyances is being adjusted to reflect Revised Baseline Schedule (RBS) Revision 4 and will be reflected in a subsequent report.
2. The term "Approved" is defined as land right conveyances with Director of Real Property for signature, PG&E for signature, or recorded.

CONSTRUCTION PACKAGE 1 (CP 1) OVERVIEW

CP 1 – Design-Build Contract Summary⁽¹⁾

Milestones

Milestone	Date
Request for Quote (RFQ) Date:	11/15/2011
Statement of Qualification (SOQ) Date:	12/19/2011
Request for Proposal (RFP) Date:	03/22/2012
Proposal:	01/18/2013
Bid Open Date:	04/13/2013
Award Date:	08/16/2013
Notice to Proceed (NTP) 1 Date:	10/15/2013
Notice to Proceed (NTP) 2 Date:	11/22/2013
Notice to Proceed (NTP) 3 Date:	07/11/2014
Original Completion Date:	03/31/2018
Current Forecast Contract Completion Date ⁽²⁾ :	03/05/2026 ⁽⁵⁾
Current Forecast Construction Completion Date⁽²⁾:	12/31/2025

Contract Value

Description	Amount
Fixed Bid Price:	\$969,988,000.00
Provisional Sums:	\$53,000,000.00
Original Contract Price:	\$1,022,988,000.00
Executed Change Orders:	\$2,092,283,967.76
Current Contract Amount ⁽⁴⁾ :	\$3,115,271,967.76
Approved Invoices to Date:	\$1,926,309,254.56
Remaining Contract Balance:	\$1,188,962,713.20

Contract Time Status

Description	Duration
Original Contract Days:	1,628
Extension of Time Awarded ⁽³⁾ :	2,832
Current Forecast Contract Days ⁽³⁾ :	4,460
Calendar Days Worked (thru 01/31/2023):	3,395

Expended to Date

Description	Percentage
Time ⁽³⁾ :	76.1%
Dollars ⁽⁴⁾ :	61.8%

Growth Percentage


Description	Percentage
Time ⁽³⁾ :	174.0%
Dollars ⁽⁴⁾ :	204.5%

Notes:

- Information in this section is coming from data provided by the PCM – Monthly Status Report.
- Updated per the conditionally accepted Revised Baseline Schedule (RBS) Revision 4.
- Contract Time Status (Extension of Time Awarded and Current Contract Days), Expended to Date (Time), and Growth Percentage (Time) calculation is based on the Current Forecast Construction Completion Date.
- Contract value will be updated to reflect RBS Revision 4 once the cost loaded schedule is received and agreed with the contractor.
- Date adjusted to account for Holidays.

CP 1 – Design-Build Expenditures

CP 1 – Monthly Expenditures (\$ Millions)

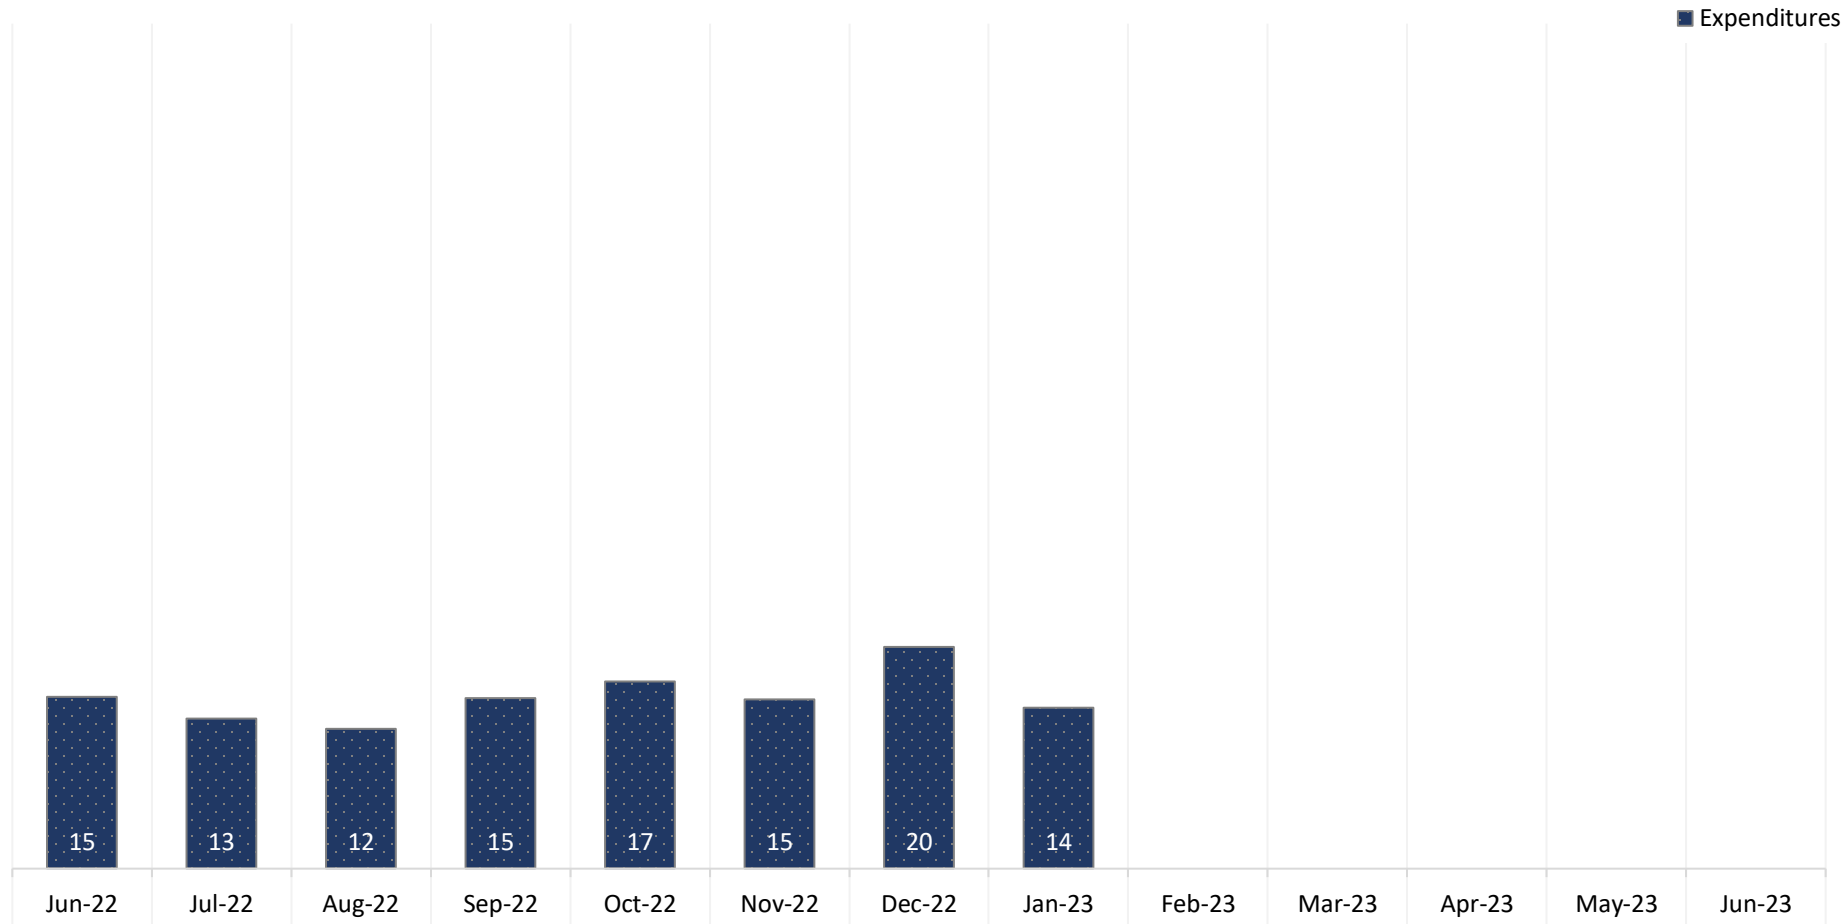

Notes:

1. Expenditures in the chart above are specific to the Design-Builder production and based on the Capital Outlay and Expenditure Report.
2. Expenditures totaled \$14.3M.


CP 1 – Change Orders (CO)

CP 1 – Change Order Status

CO Number	Title	Change Status	Amount	Executed Date
00130	Madera Irrigation District (MID) Changes – Design	Executed	\$140,845.00	01-30-23
00471	East Church Ave HST/UPRR and BNSF Overcrossing - Material Only	Executed	\$4,740,836.00	01-17-23
00472	Shaw and Cornelia Intersection Revisions Due to COF – Design	Executed	\$119,411.00	01-30-23
00478	Downtown Fresno, Tulare, Ventura Streets UPRR Bridges – Construction	Executed	\$74,203,857.00	01-31-23
00479	CN 1333 - Archaeological Discovery at Belmont and Weber Ave	Executed	\$2,453.00	01-13-23
00481	Additional Concrete Liner at Dry Creek Canal – Construction	Executed	\$182,743.00	01-10-23
TOTAL			\$79,390,145.00	

CP 1 – Risk Contingency

CP 1 – Risk Contingency Status (\$ Millions)

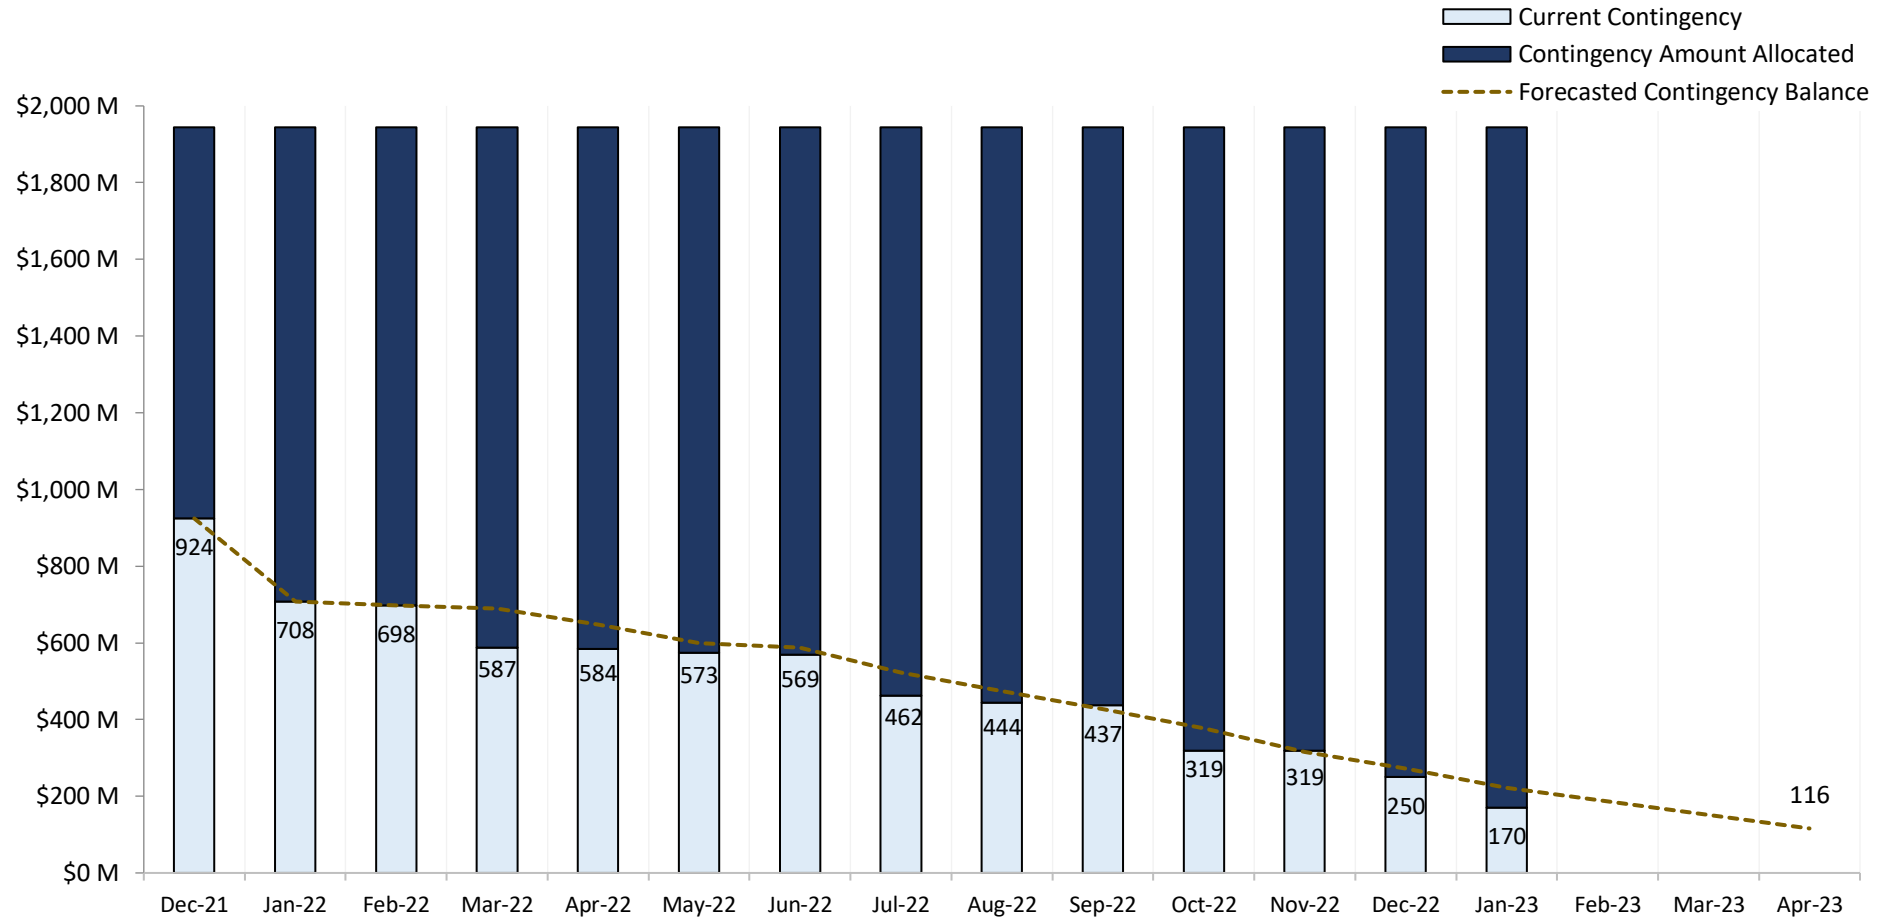


Notes:

1. Program baseline is \$1,945M.
2. Contingency balance updated to reflect the Board’s adoption of Resolution #HSR21-11 (Expenditure Authorization Increase).
3. Contingency Amount Allocated reflects executed change orders and Business Oversight Committee (BOC) approved items.
4. The Forecasted Contingency Balance drawdown curve is based only on agreed change orders expected to be executed within the three-month window. Due to change order negotiations and dispute resolution, timing and value of Forecasted Contingency Balance is uncertain.

CP 1 – Monthly Construction Labor

CP 1 – Monthly Construction Workforce Total – Actual (FTE)

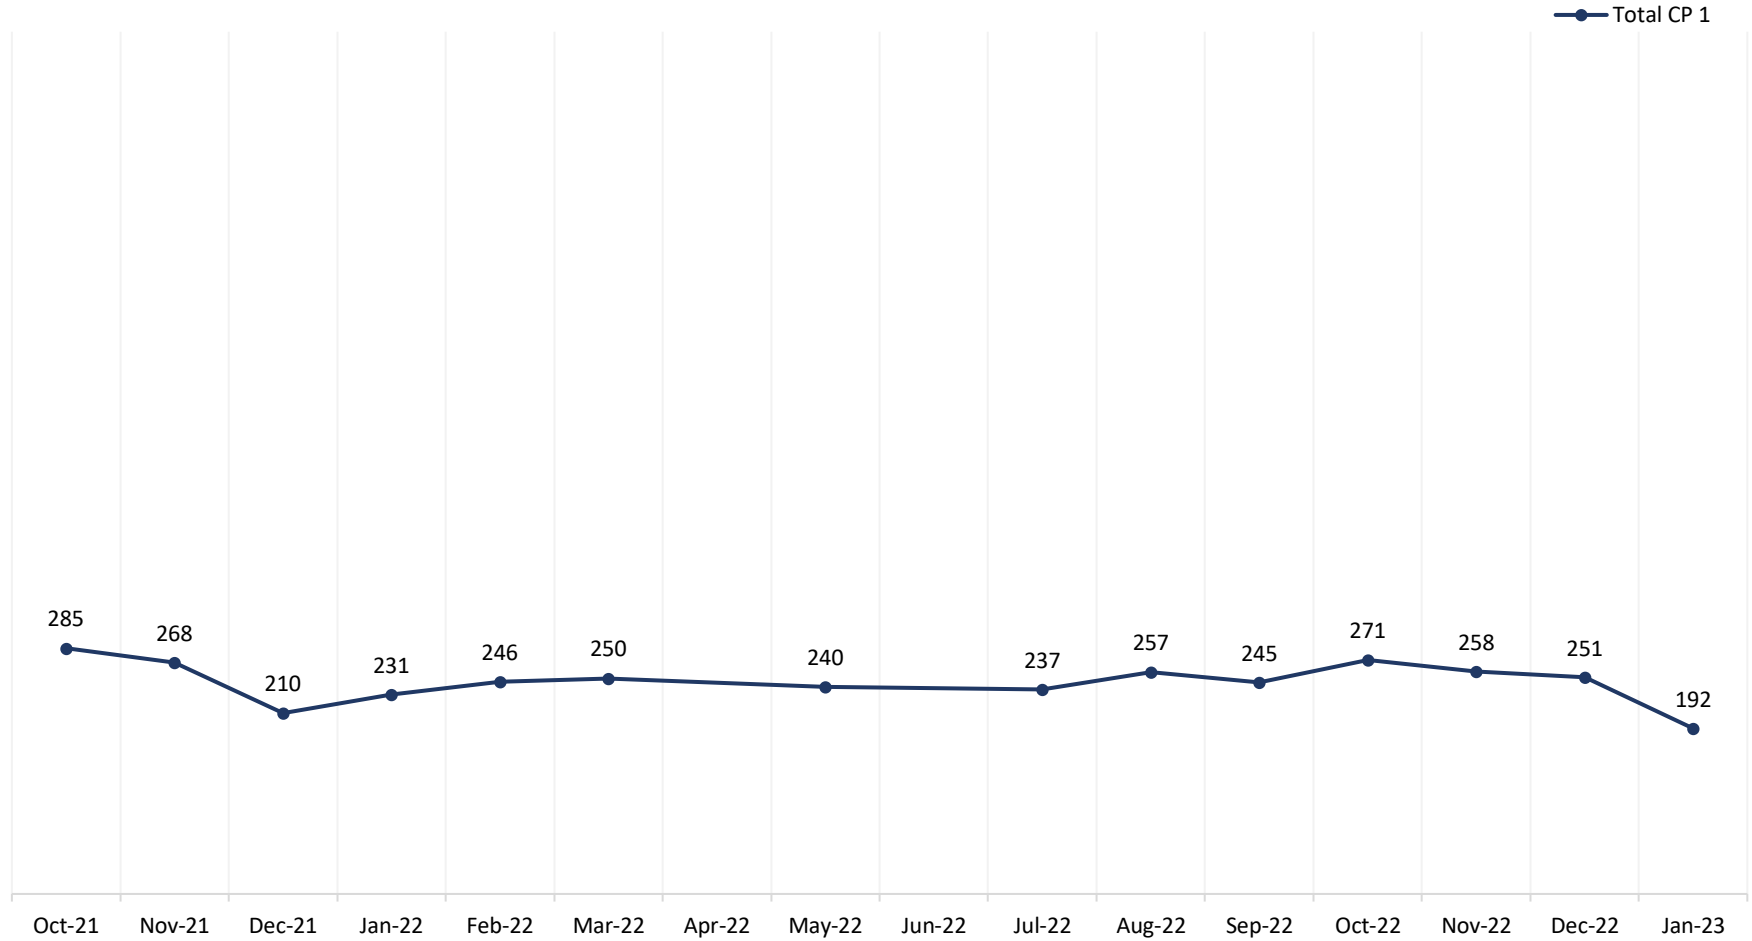


Notes:


1. The construction labor numbers (full-time employees) are based on the weekly totals divided by the number of weeks within the working calendar month and represents the Average Daily Site Workers (by week).
2. A decrease of 59 workers from the previous month (251).
3. Decrease in labor numbers due to multiple rain events.

CP 1 – Construction Progress

CP 1 – Construction Progress

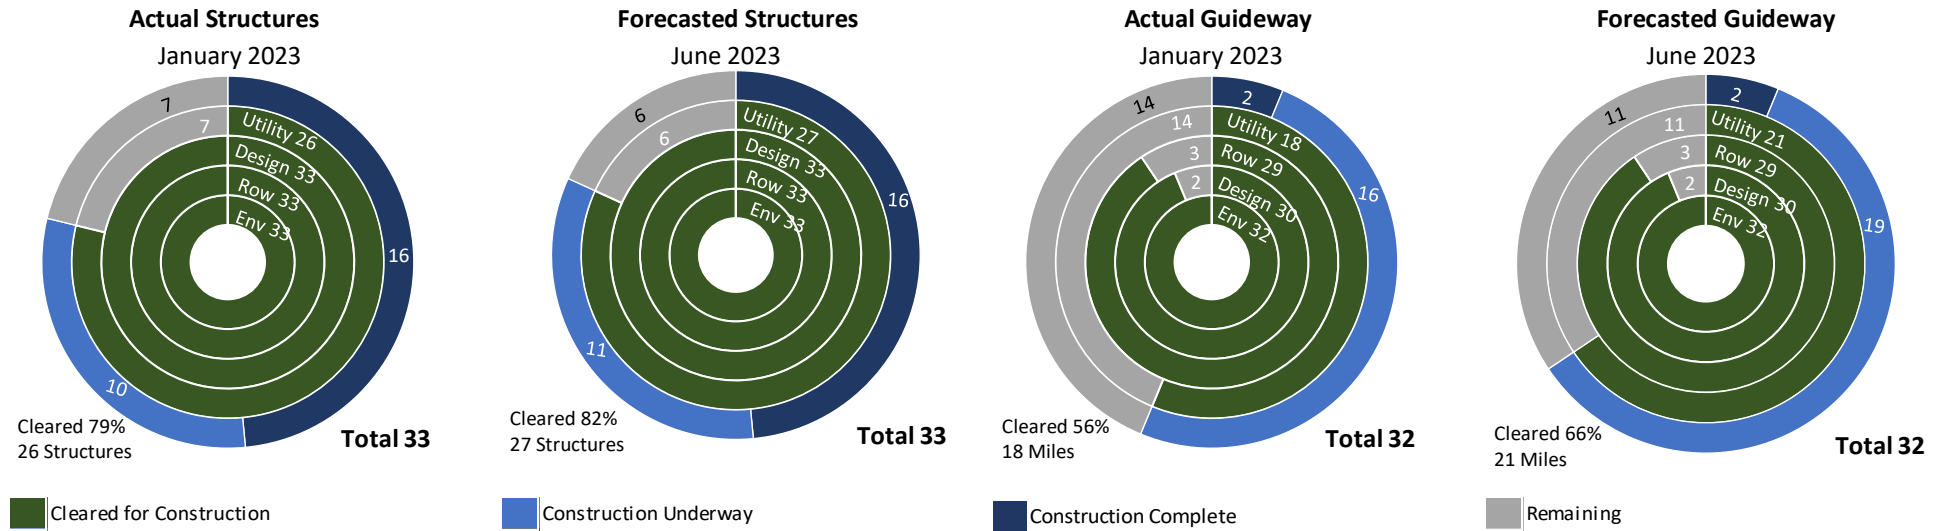

CP 1 – Structures and Guideway Progress – Forecast vs. Actual

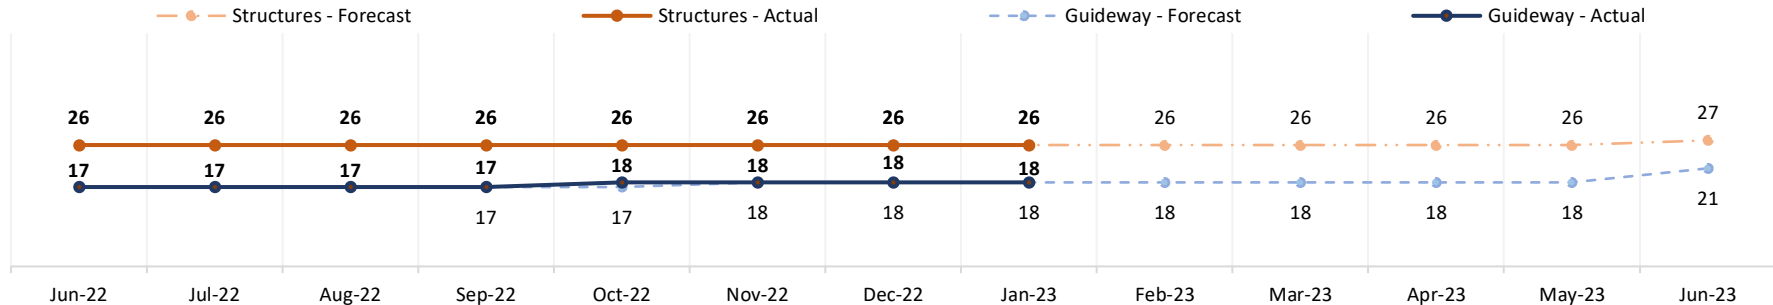


- Notes:**
- The circle charts above incorporate Revised Baseline Schedules (RBS) Revision 4 data as of September 2022, pending final approval.
 - The line chart above incorporates provisional forecast numbers as of September 2022, pending final approval of RBS Revision 4.
 - Construction Complete definition:
 - Structure Completion – all concrete work is complete.
 - Guideway Completion – earthworks complete with rough grading.
 - Total Structures: 33:
 - 26 structures underway/construction complete.
 - Total Guideway: 32 miles:
 - 18 miles underway/construction complete.
 - There are 32 miles of guideway approved by the Authority, but 2.5 miles (Caltrans section) has not been approved by Union Pacific Railroad (UPRR). **Update:** UPRR has approved the Caltrans 2.5 miles at 60% Design. The IPB Work Plan has been approved and work is starting February 2023.
 - Late finish dates are being used to estimate forecast numbers.

CP 1– Real Property/Right-of-Way (ROW)

CP 1 – Right-of-Way (ROW) Summary

Construction Package	Total Needed Parcels January 31, 2023	Total Parcels Delivered to Date January 31, 2023	Remaining Parcels to be Delivered January 31, 2023
CP 1	1,082	1,058	24

CP 1 – Parcel Delivery to Design-Builder (DB) Summary

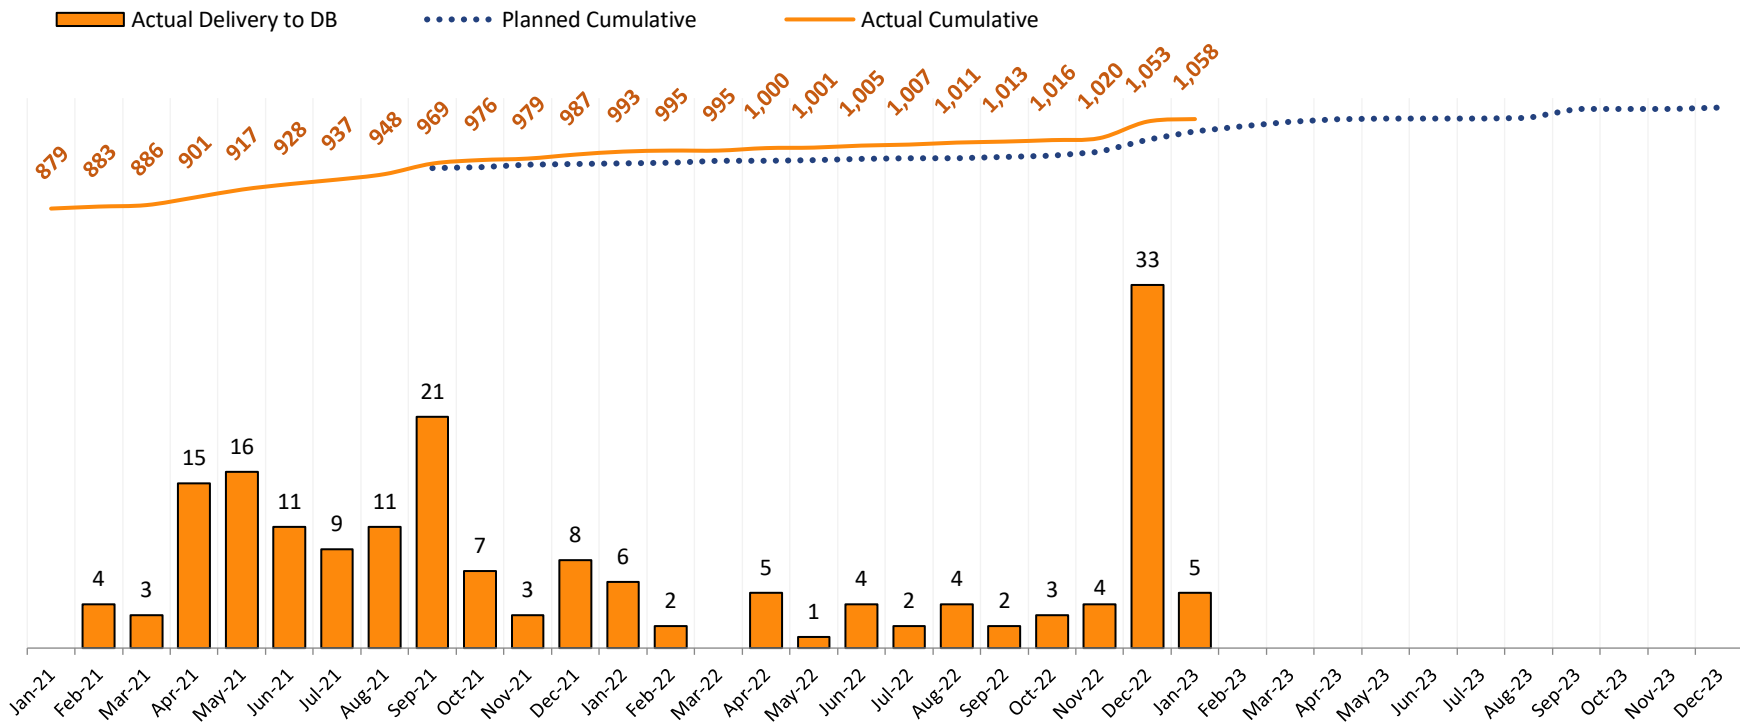

Notes:


1. This reflects the actual parcels delivered to the Design-Builder by month and provisional forecasts as of September 2022 pending final approval of Revised Baseline Schedules (RBS) Revision 4.
2. Total Needed Parcels was reduced by one parcel in CP 1.

CP 1 – Real Property/Right-of-Way (ROW) Railroad

CP 1 – Right-of-Way (ROW) Railroad Summary

Construction Package	Total Needed Railroad Parcels January 31, 2023	Total Railroad Parcels Delivered to Date January 31, 2023	Remaining Railroad Parcels to be Delivered January 31, 2023
CP 1	83	63	20

CP 1 – Railroad Parcel Delivery to Design-Builder (DB) Summary

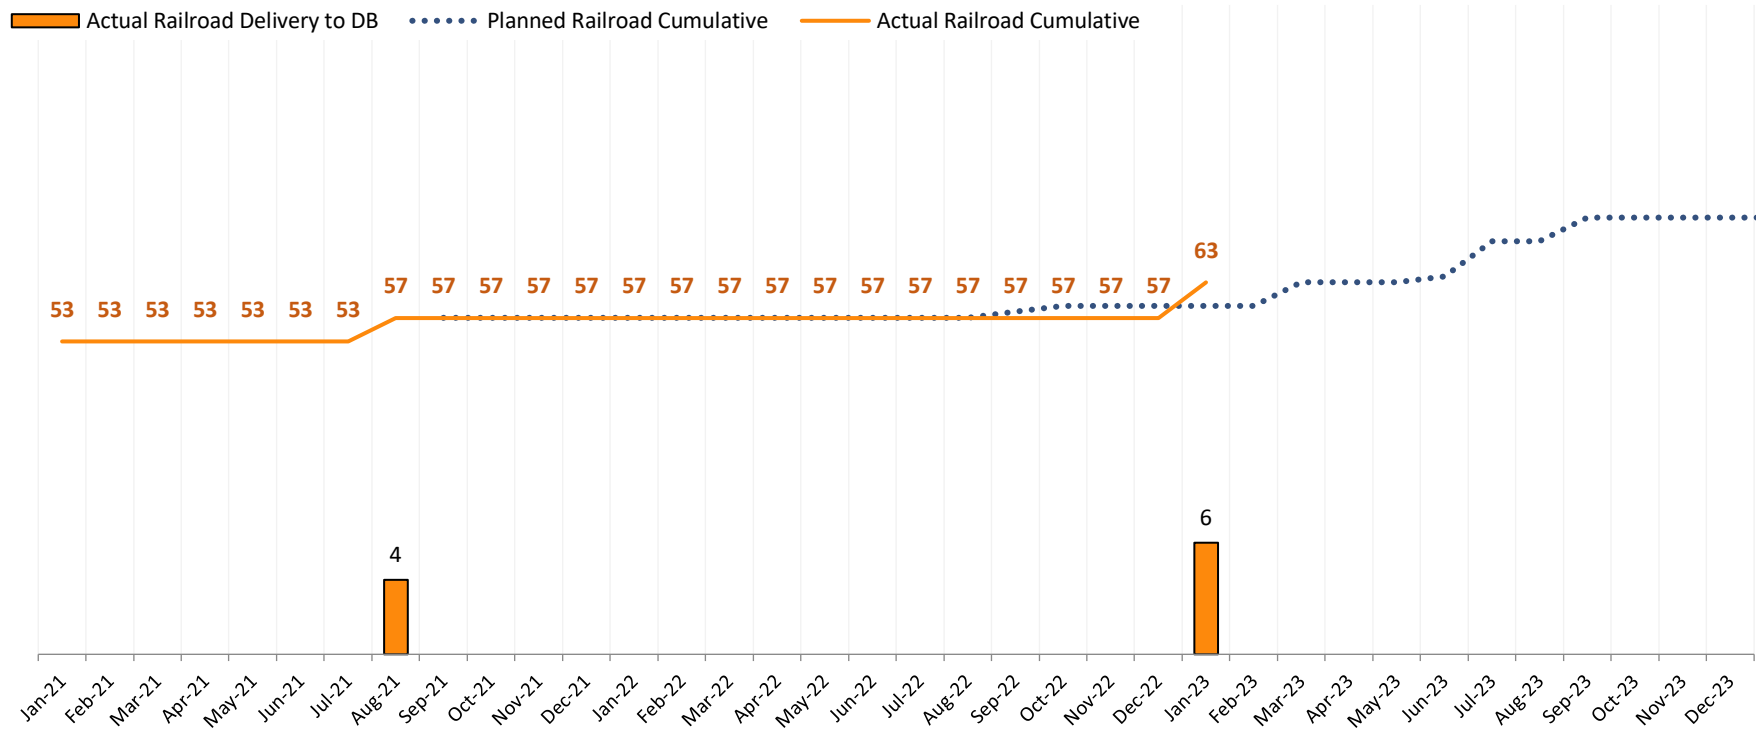

Note:


1. The Planned Cumulative line for Railroad Parcel Delivery reflects provisional forecasts as of September 2022 pending final approval of Revised Baseline Schedules (RBS) Revision 4.
2. Two Railroad parcel delivery dates are being reforecast, not impacting the critical path.

CP 1 – Tier 1 Land Right Conveyances Required Prior to Construction (PG&E, SCE, FID, FMFCD)

CP 1 – Tier 1 Land Right Conveyances Required Prior to Construction (PG&E, SCE, FID, FMFCD) Summary

Construction Package	Total Needed Land Right Conveyances January 31, 2023	Total Land Right Conveyances Approved ⁽²⁾ to Date January 31, 2023	Remaining Land Right Conveyances to be Approved January 31, 2023
CP 1	393	344	49

CP 1 – Tier 1 Land Right Conveyances Required Prior to Construction (PG&E, SCE, FID, FMFCD) Summary

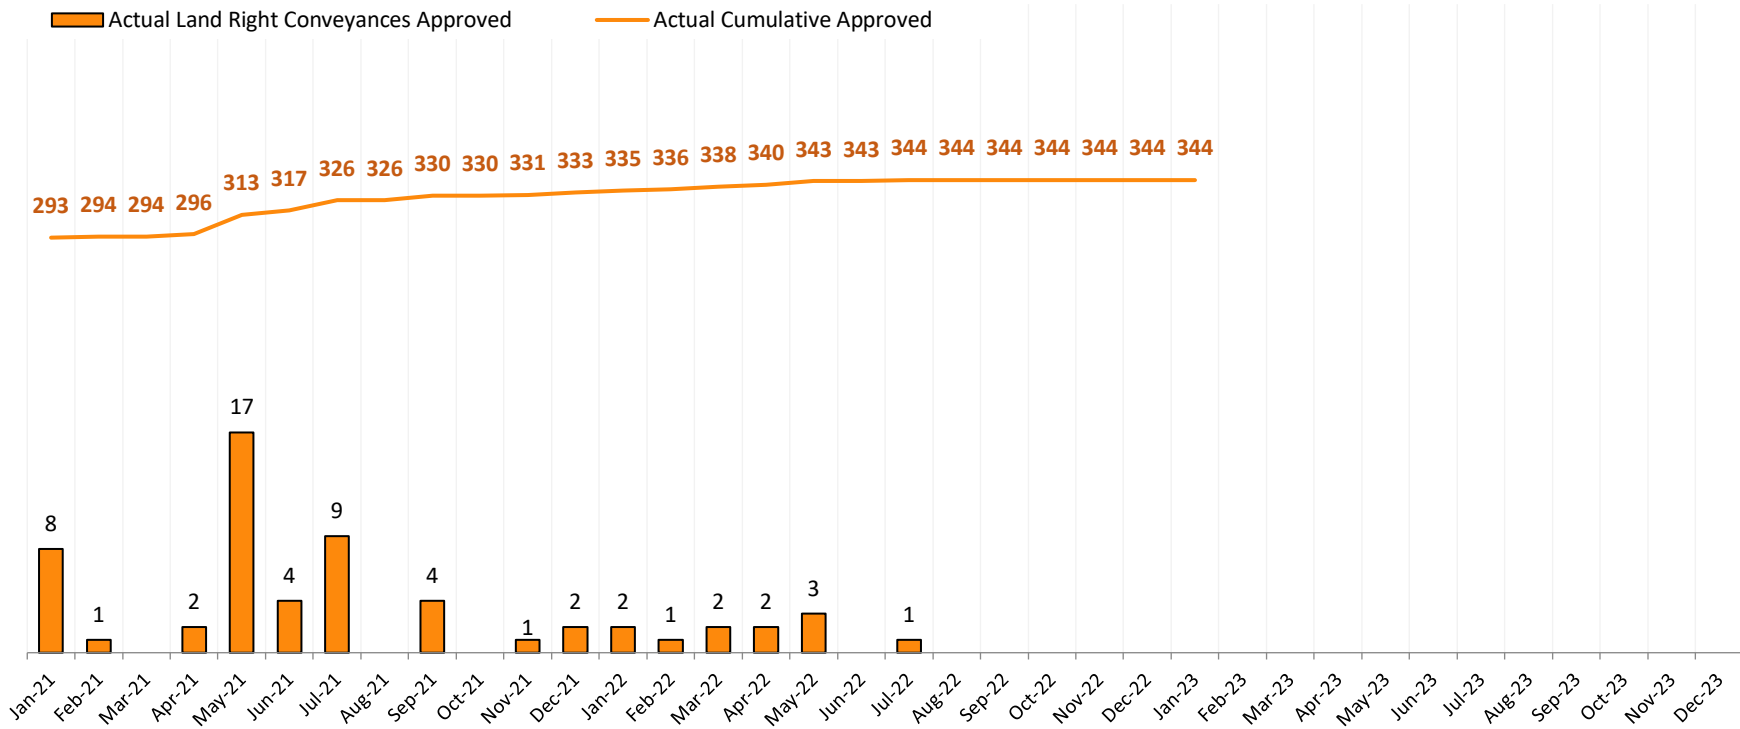

Notes:

1. The Planned Cumulative line for Land Right Conveyances is being adjusted to reflect Revised Baseline Schedule (RBS) Revision 4 and will be reflected in a subsequent report.
2. The term "Approved" is defined as land right conveyances with Director of Real Property for signature, PG&E for signature, or recorded.

CONSTRUCTION PACKAGE 2-3 (CP 2-3) OVERVIEW

CP 2-3 – Design-Build Contract Summary⁽¹⁾

Milestones

Milestone	Date
Request for Quote (RFQ) Date:	10/09/2013
Statement of Qualification (SOQ) Date:	12/13/2013
Request for Proposal (RFP) Date:	04/03/2014
Proposal:	10/30/2014
Bid Open Date:	12/11/2014
Award Date:	06/10/2015
Late Notice to Proceed (LNTP) Date:	06/12/2015
Notice to Proceed (NTP) Date:	07/25/2015
Original Completion Date:	08/19/2019
Current Forecast Contract Completion Date ⁽²⁾ :	05/21/2026
Current Forecast Construction Completion Date⁽²⁾:	03/21/2026

Contract Value

Description	Amount
Fixed Bid Price:	\$1,205,335,890.00
Provisional Sums:	\$160,000,000.00
Original Contract Price:	\$1,365,335,890.00
Executed Change Orders:	\$1,509,693,078.59
Current Contract Amount ⁽⁴⁾ :	\$2,875,028,968.59
Approved Invoices to Date:	\$1,875,771,023.87
Remaining Contract Balance:	\$999,257,944.72

Contract Time Status

Description	Duration
Original Contract Days:	1,486
Extension of Time Awarded ⁽³⁾ :	2,406
Current Forecast Contract Days ⁽³⁾ :	3,892
Calendar Days Worked (thru 01/31/2023):	2,747

Expended to Date Percentage

Description	Percentage
Time ⁽³⁾ :	70.6%
Dollars ⁽⁴⁾ :	65.2%

Growth Percentage


Description	Percentage
Time ⁽³⁾ :	161.9%
Dollars ⁽⁴⁾ :	110.6%

Notes:

- Information in this section is coming from data provided by the PCM – Monthly Status Report.
- Updated per the conditionally accepted Revised Baseline Schedule (RBS) Revision 4.
- Contract Time Status (Extension of Time Awarded and Current Contract Days), Expended to Date (Time), and Growth Percentage (Time) calculation is based on the Current Forecast Construction Completion Date.
- Contract value will be updated to reflect RBS Revision 4 once the cost loaded schedule is received and agreed with the contractor.

CP 2-3 – Design-Build Expenditures

CP 2-3 – Monthly Expenditures (\$ Millions)

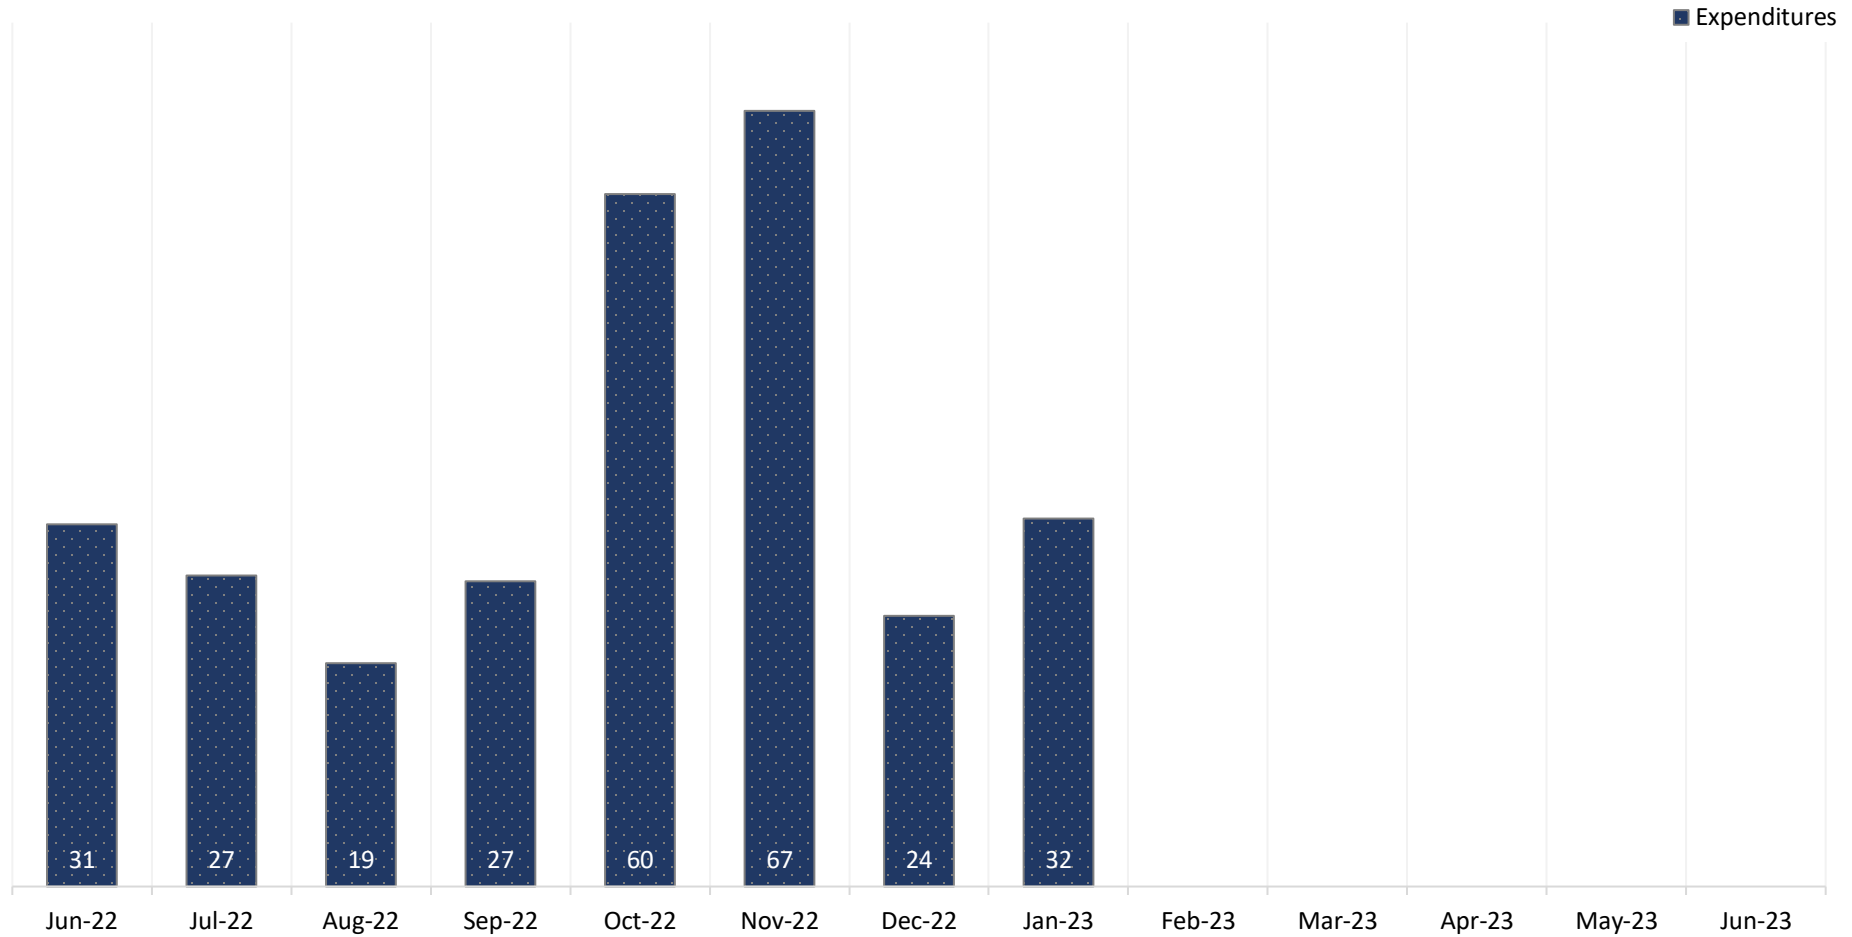

Notes:

1. Expenditures in the chart above are specific to the Design-Builder production and based on the Capital Outlay and Expenditure Report.
2. Expenditures totaled \$31.9M.


CP 2-3 – Change Orders (CO)

CP 2-3 – Change Order Status

CO Number	Title	Change Status	Amount	Executed Date
00348	Tied Arch Bridge at SR 43-Superstructure – Falsework and Formwork	Executed	\$1,034,160.00	01-27-23
00345	Hanford Armona Overhead to Underground SCE Utility Relocation	Executed	\$1,645,770.00	01-09-23
00372	Kings County Pothole Repair and Related Ancillary Work on Overhead Structures - T&M	Executed	\$100,000.00	01-09-23
00045.37	Escalation Costs - September 2022	Executed	\$2,185,655.00	01-03-23
TOTAL			\$4,965,585.00	

CP 2-3 – Risk Contingency

CP 2-3 – Risk Contingency Status (\$ Millions)

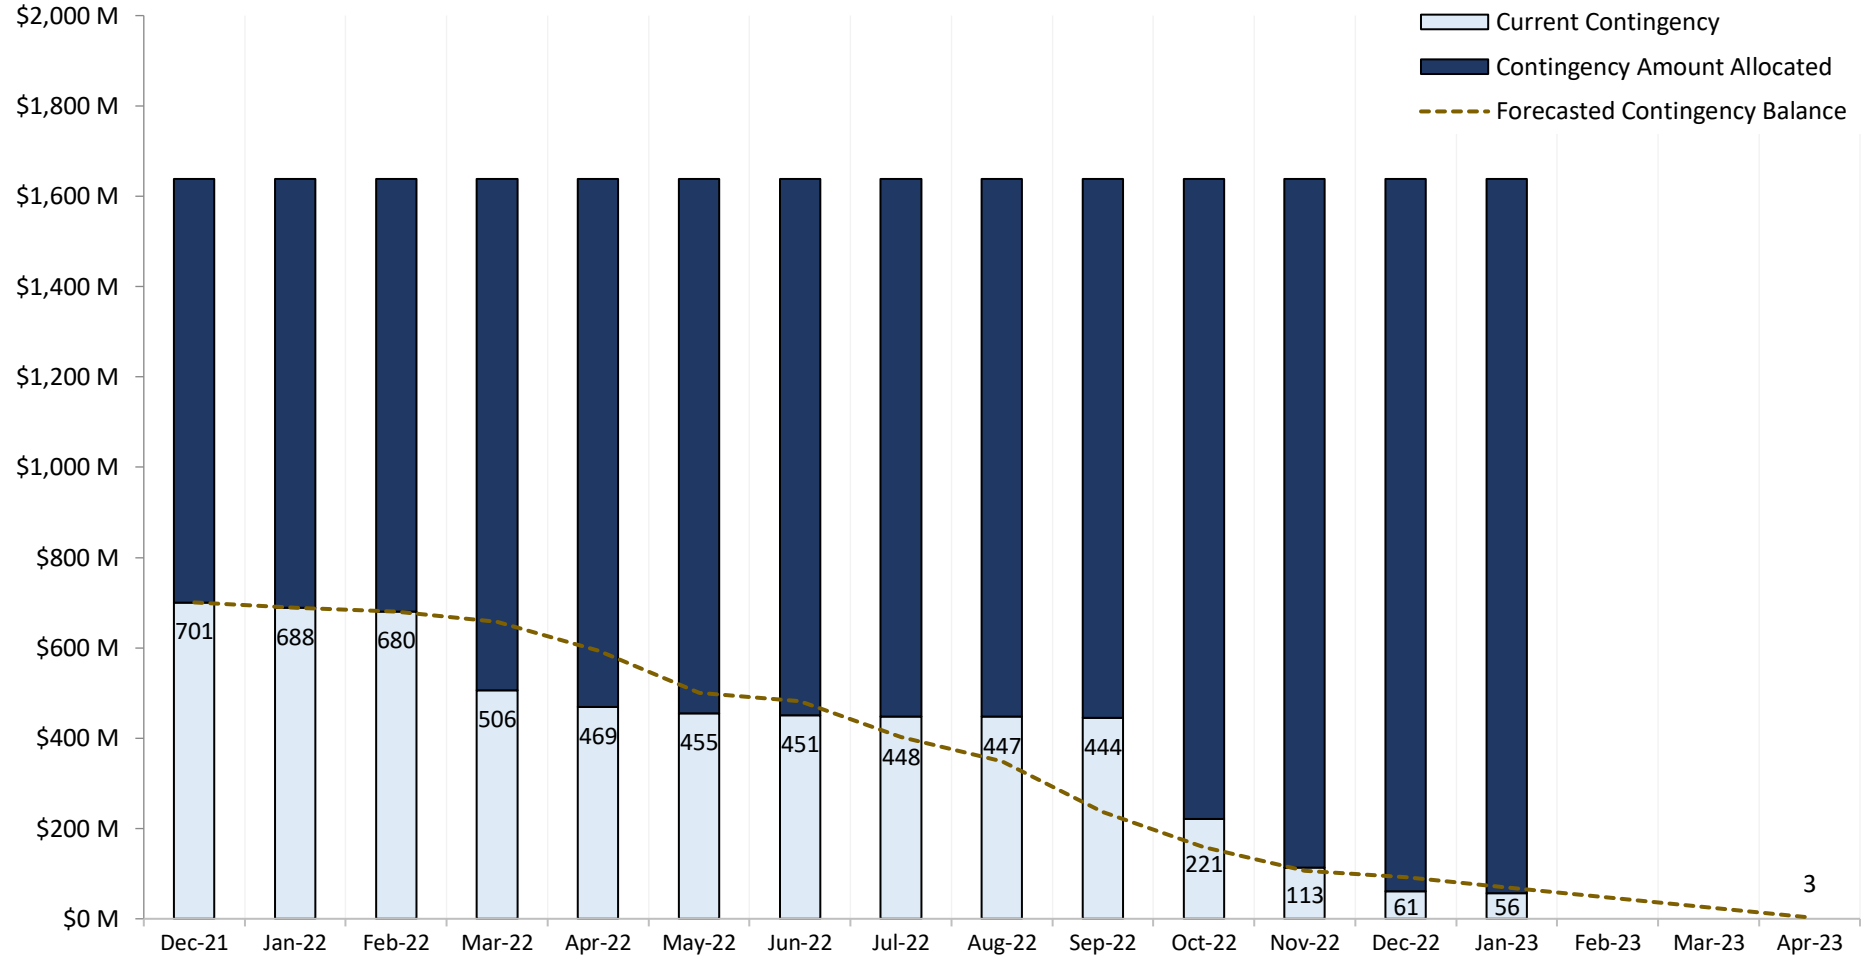


Notes:

1. Program baseline is \$1,638M.
2. Contingency balance updated to reflect the Board’s adoption of Resolution #HSR21-11 (Expenditure Authorization Increase).
3. Contingency Amount Allocated reflects executed change orders and Business Oversight Committee (BOC) approved items.
4. The Forecasted Contingency Balance drawdown curve is based only on agreed change orders expected to be executed within the three-month window. Due to change order negotiations and dispute resolution, timing and value of Forecasted Contingency Balance is uncertain.

CP 2-3 – Monthly Construction Labor

CP 2-3 – Monthly Construction Workforce Total – Actual (FTE)

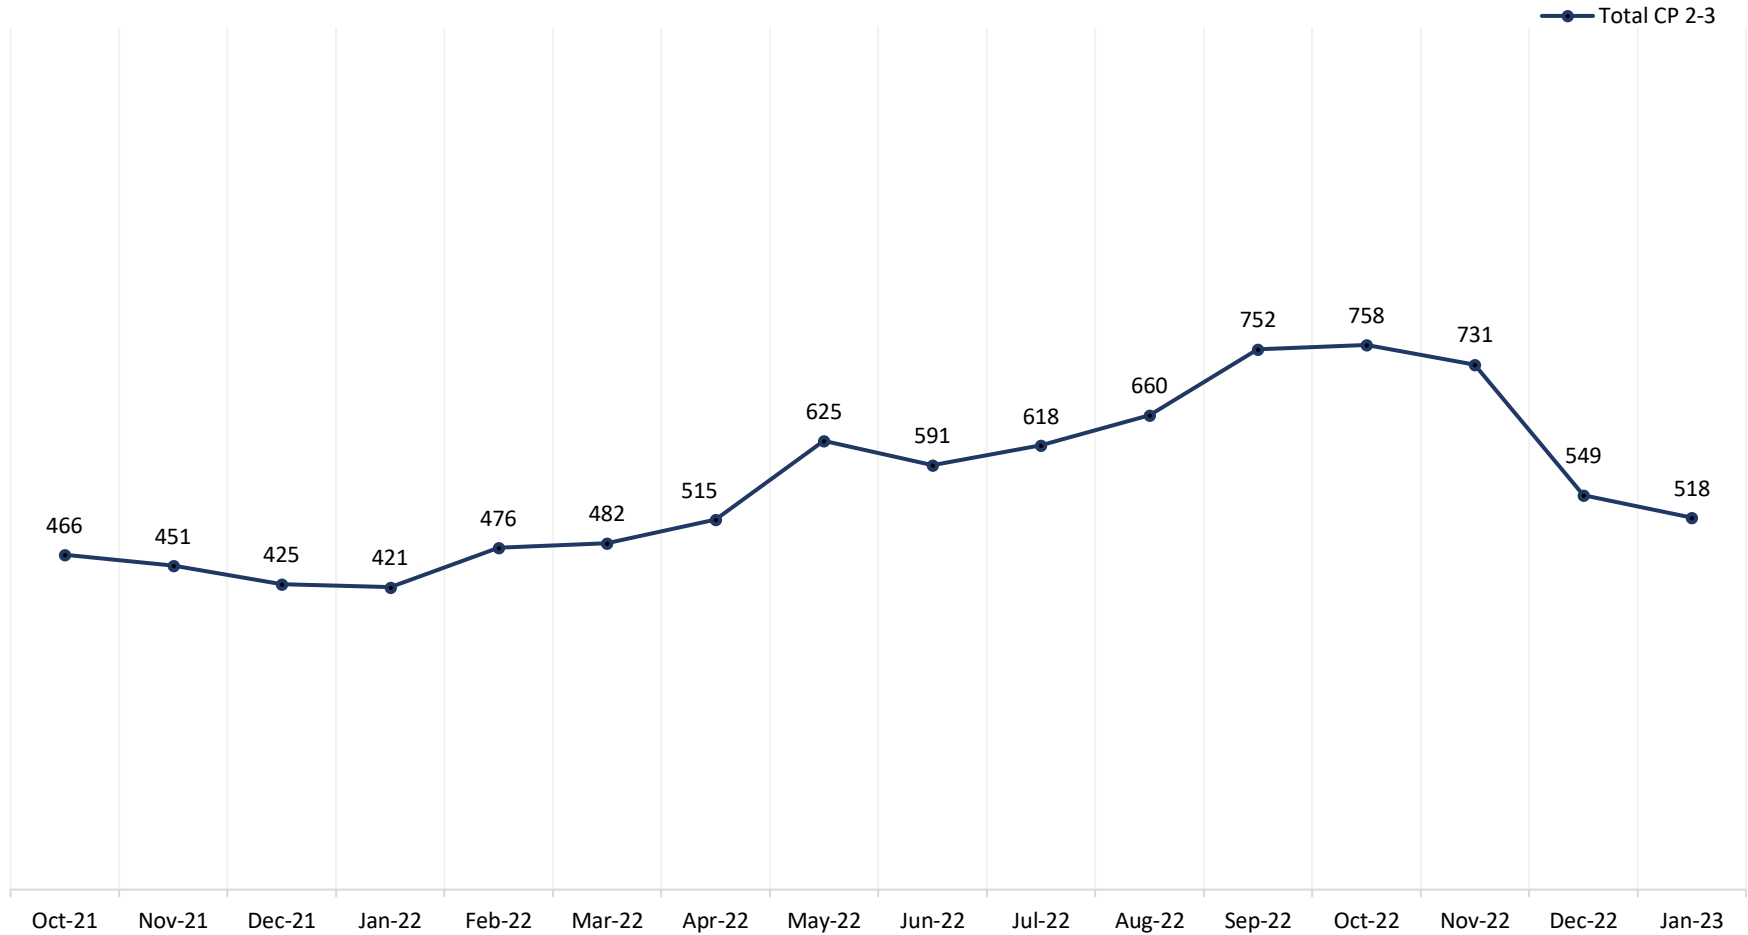


Notes:


1. The construction labor numbers (full-time employees) are based on the weekly totals divided by the number of weeks within the working calendar month and represents the Average Daily Site Workers (by week).
2. A decrease of 31 workers from the previous month (549).
3. Decrease in labor numbers due to multiple rain events.

CP 2-3 – Construction Progress

CP 2-3 – Construction Progress

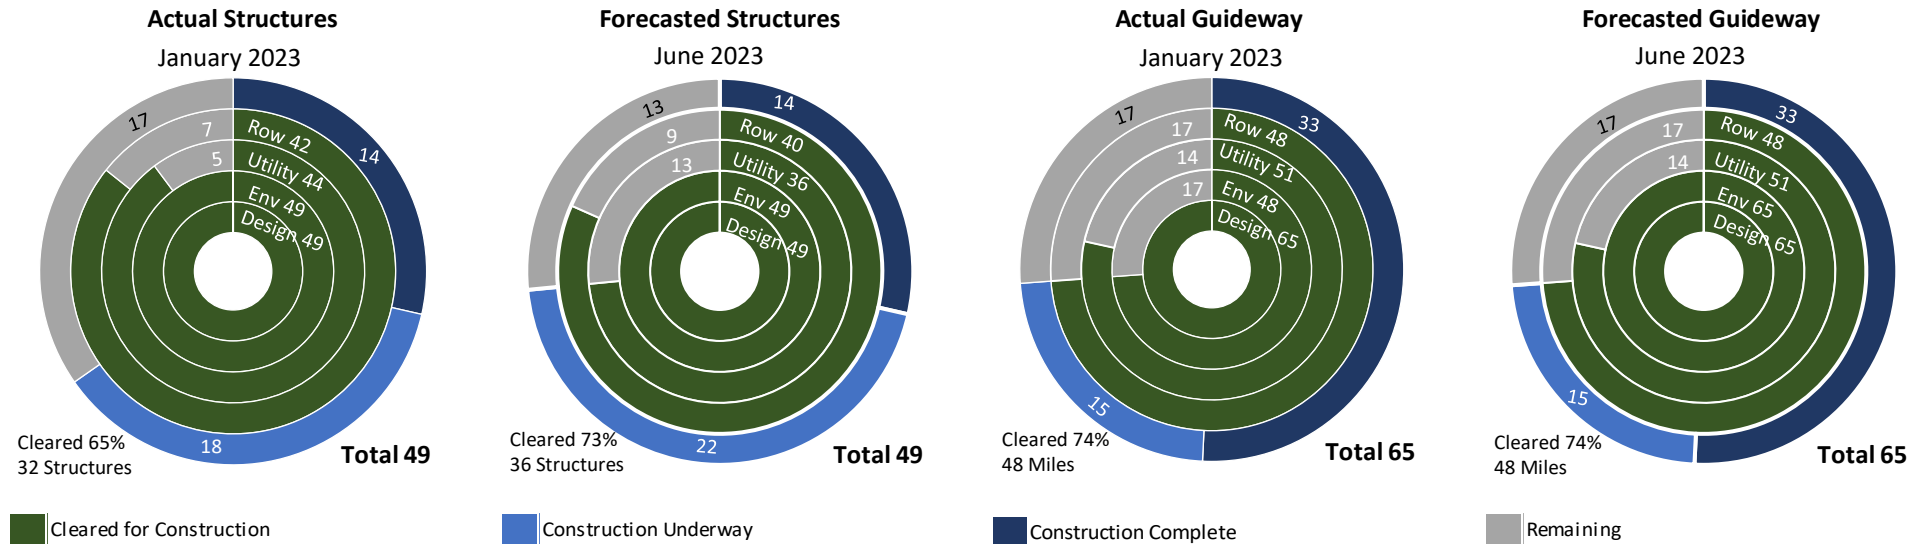

CP 2-3 – Structures and Guideway Progress – Forecast vs. Actual

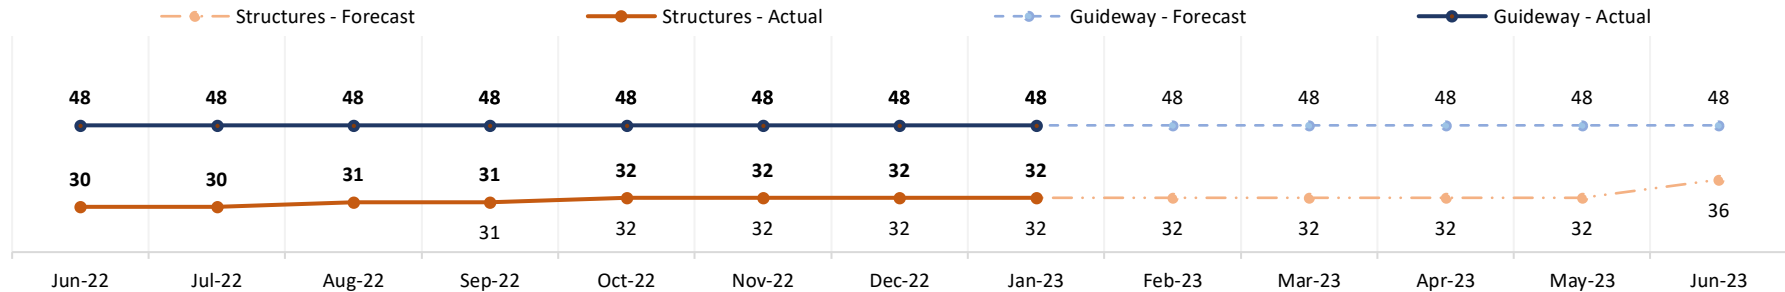

Notes:


- The circle charts above incorporate Revised Baseline Schedules (RBS) Revision 4 data as of September 2022, pending final approval.
- The line chart above incorporates provisional forecast numbers as of September 2022, pending final approval of RBS Revision 4.
- Construction Complete definition:
 - Structure Completion – all concrete work is complete.
 - Guideway Completion – earthworks complete with rough grading.
- Total Structures: 49:
 - 32 structures underway/construction complete.
- Total Guideway: 65 miles:
 - 48 miles underway/construction complete.
- Late finish dates are being used to estimate forecast numbers.

CP 2-3 – Real Property/Right-of-Way (ROW)

CP 2-3 – Right-of-Way (ROW) Summary

Construction Package	Total Needed Parcels January 31, 2023	Total Parcels Delivered to Date January 31, 2023	Remaining Parcels to be Delivered January 31, 2023
CP 2-3	986	935	51

CP 2-3 – Parcel Delivery to Design-Builder (DB) Summary

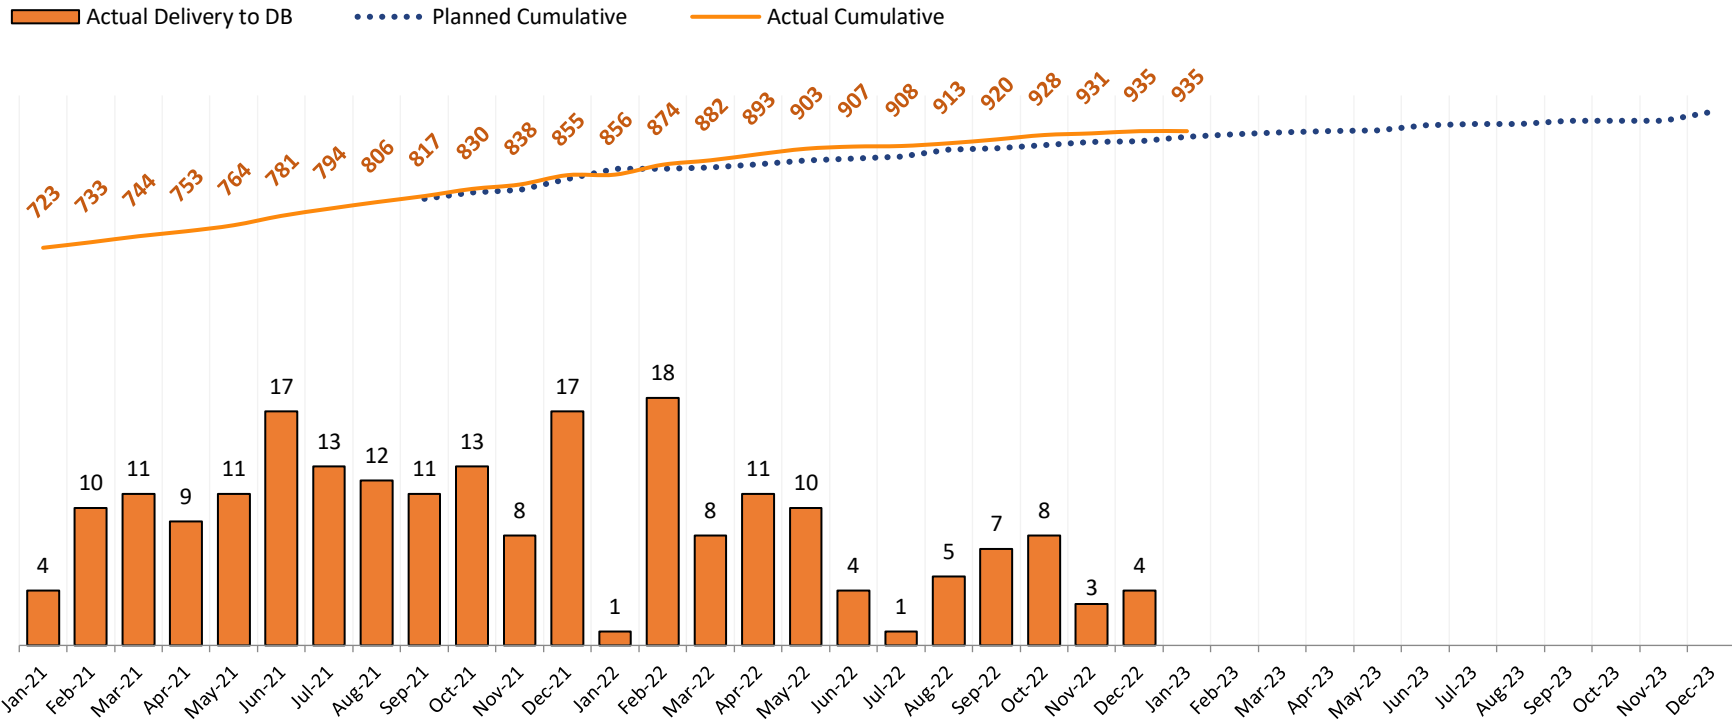

Notes:


1. This reflects the actual parcels delivered to the Design-Builder by month and forecasts based on Revised Baseline Schedules (RBS) Revision 4.

CP 2-3 – Real Property/Right-of-Way (ROW) Railroad

CP 2-3 – Right-of-Way (ROW) Railroad Summary

Construction Package	Total Needed Railroad Parcels January 31, 2023	Total Railroad Parcels Delivered to Date January 31, 2023	Remaining Railroad Parcels to be Delivered January 31, 2023
CP 2-3	58	51	7

CP 2-3 – Railroad Parcel Delivery to Design-Builder (DB) Summary

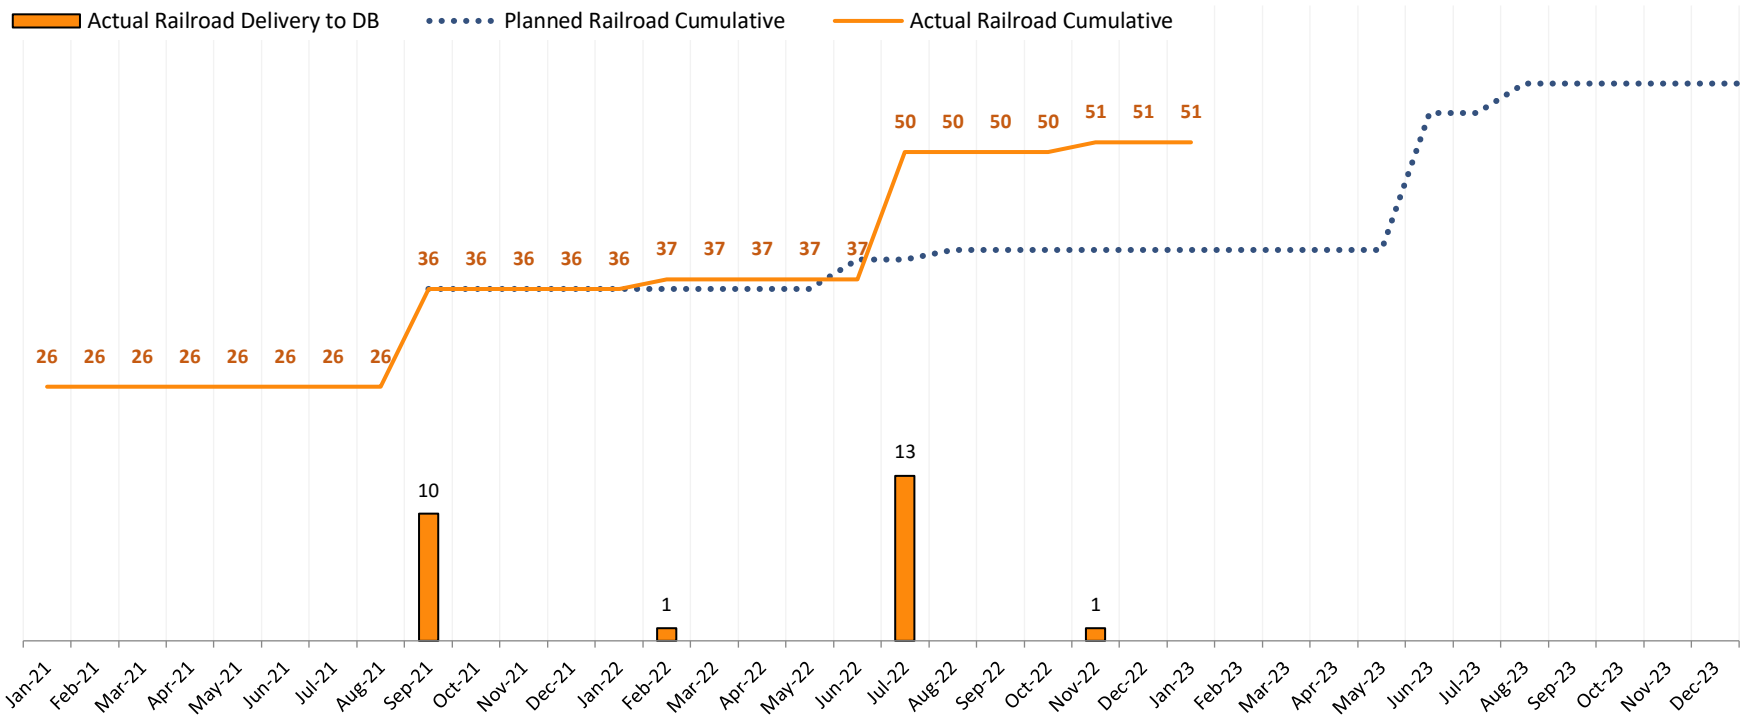

Notes:


1. This reflects the actual Railroad parcels delivered to the Design-Builder by month and forecasts based on Revised Baseline Schedules (RBS) Revision 4.

CP 2-3 – Tier 1 Land Right Conveyances Required Prior to Construction (PG&E, SCE, FID, FMFCD)

CP 2-3 – Tier 1 Land Right Conveyances Required Prior to Construction (PG&E, SCE, FID, FMFCD) Summary

Construction Package	Total Needed Land Right Conveyances January 31, 2023	Total Land Right Conveyances Approved ⁽²⁾ to Date January 31, 2023	Remaining Land Right Conveyances to be Approved January 31, 2023
CP 2-3	433	280	153

CP 2-3 – Tier 1 Land Right Conveyances Required Prior to Construction (PG&E, SCE, FID, FMFCD) Summary

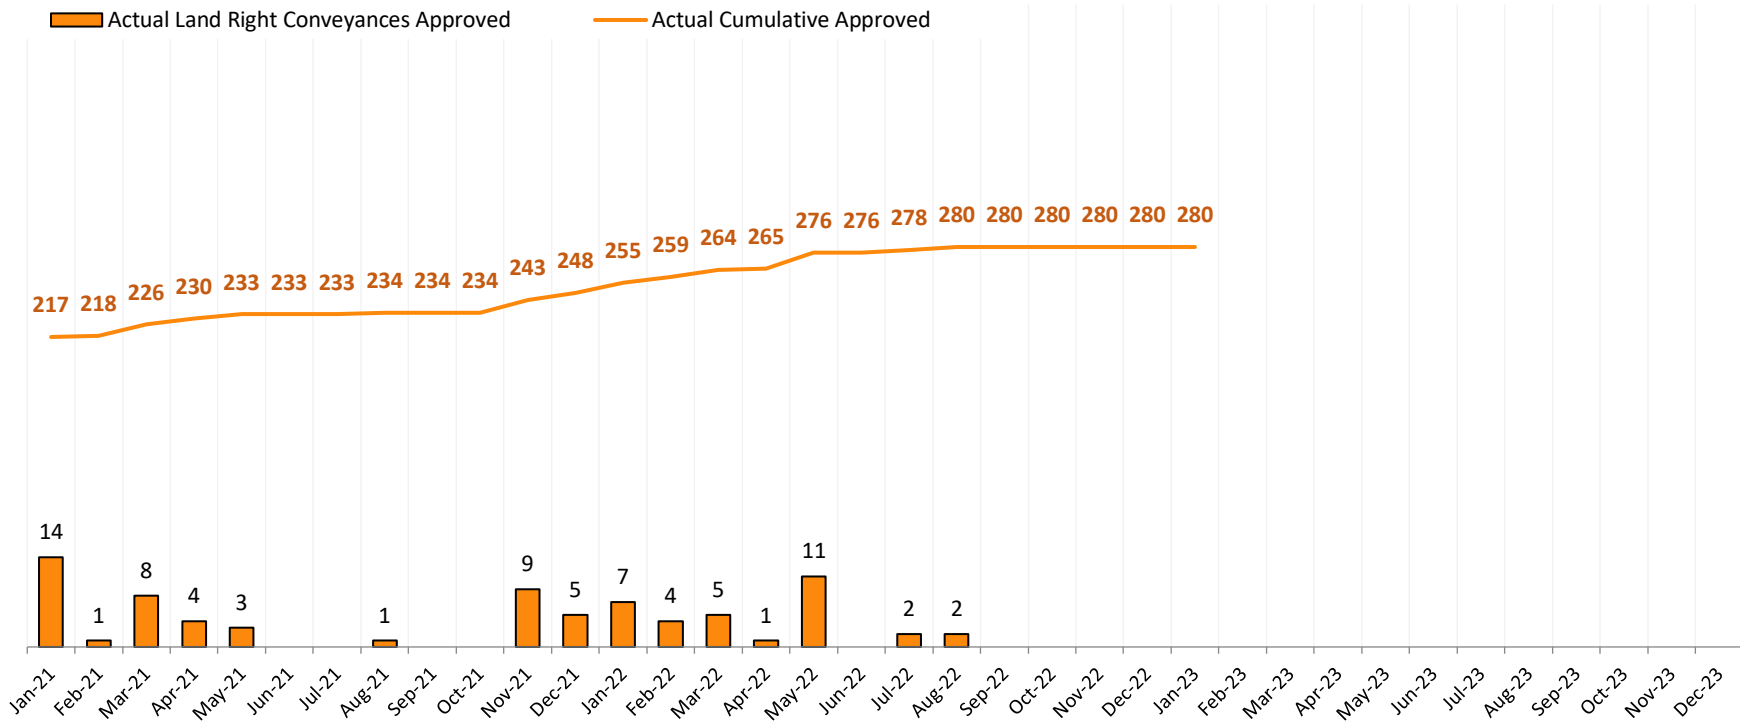

Notes:

1. The Planned Cumulative line for Land Right Conveyances is being adjusted to reflect Revised Baseline Schedule (RBS) Revision 4 and will be reflected in a subsequent report.
2. The term "Approved" is defined as land right conveyances with Director of Real Property for signature, PG&E for signature, or recorded.

CONSTRUCTION PACKAGE 4 (CP 4) OVERVIEW

CP 4 – Design-Build Contract Summary⁽¹⁾

Milestones

Milestone	Date
Request for Quote (RFQ) Date:	11/20/2014
Statement of Qualification (SOQ) Date:	01/30/2015
Request for Proposal (RFP) Date:	05/27/2015
Proposal:	11/25/2015
Bid Open Date:	01/05/2016
Award Date:	02/29/2016
Late Notice to Proceed (LNTP) Date:	03/01/2016
Notice to Proceed (NTP) Date:	04/15/2016
Original Completion Date:	06/03/2019
Current Forecast Contract Completion Date ⁽²⁾ :	10/01/2023
Current Forecast Construction Completion Date⁽³⁾:	07/24/2023

Contract Value

Description	Amount
Fixed Bid Price:	\$337,247,000.00
Provisional Sums:	\$107,000,000.00
Original Contract Price:	\$444,247,000.00
	p
Executed Change Orders:	\$275,601,996.25
Current Contract Amount:	\$719,848,996.25
Approved Invoices to Date:	\$633,515,267.98
Remaining Contract Balance:	\$86,333,728.27

Current Time Status

Description	Duration
Original Contract Days:	1,144
Extension of Time Awarded:	1,512
Current Forecast Contract Days:	2,656
Calendar Days Worked (thru 01/31/2023):	2,482

Expended to Date

Description	Percentage
Time:	93.4%
Dollars:	88.0%

Growth Percentage


Description	Percentage
Time:	132.2%
Dollars:	62.0%

Notes:

- Information in this section is coming from data provided by the PCM – Monthly Status Report.
- Updated to align with Current Forecast Contract Completion Date based on Expenditure Authorization.
- Expenditure Authorization Current Forecast Construction Completion Date of July 24, 2023.
- Contract Time Status (Extension of Time Awarded and Current Forecast Contract Days), Expended to Date (Time), and Growth Percentage (Time) calculation is based on the Current Construction Completion Date.

CP 4 – Earned Value

CP 4 – Earned Value Summary (%)

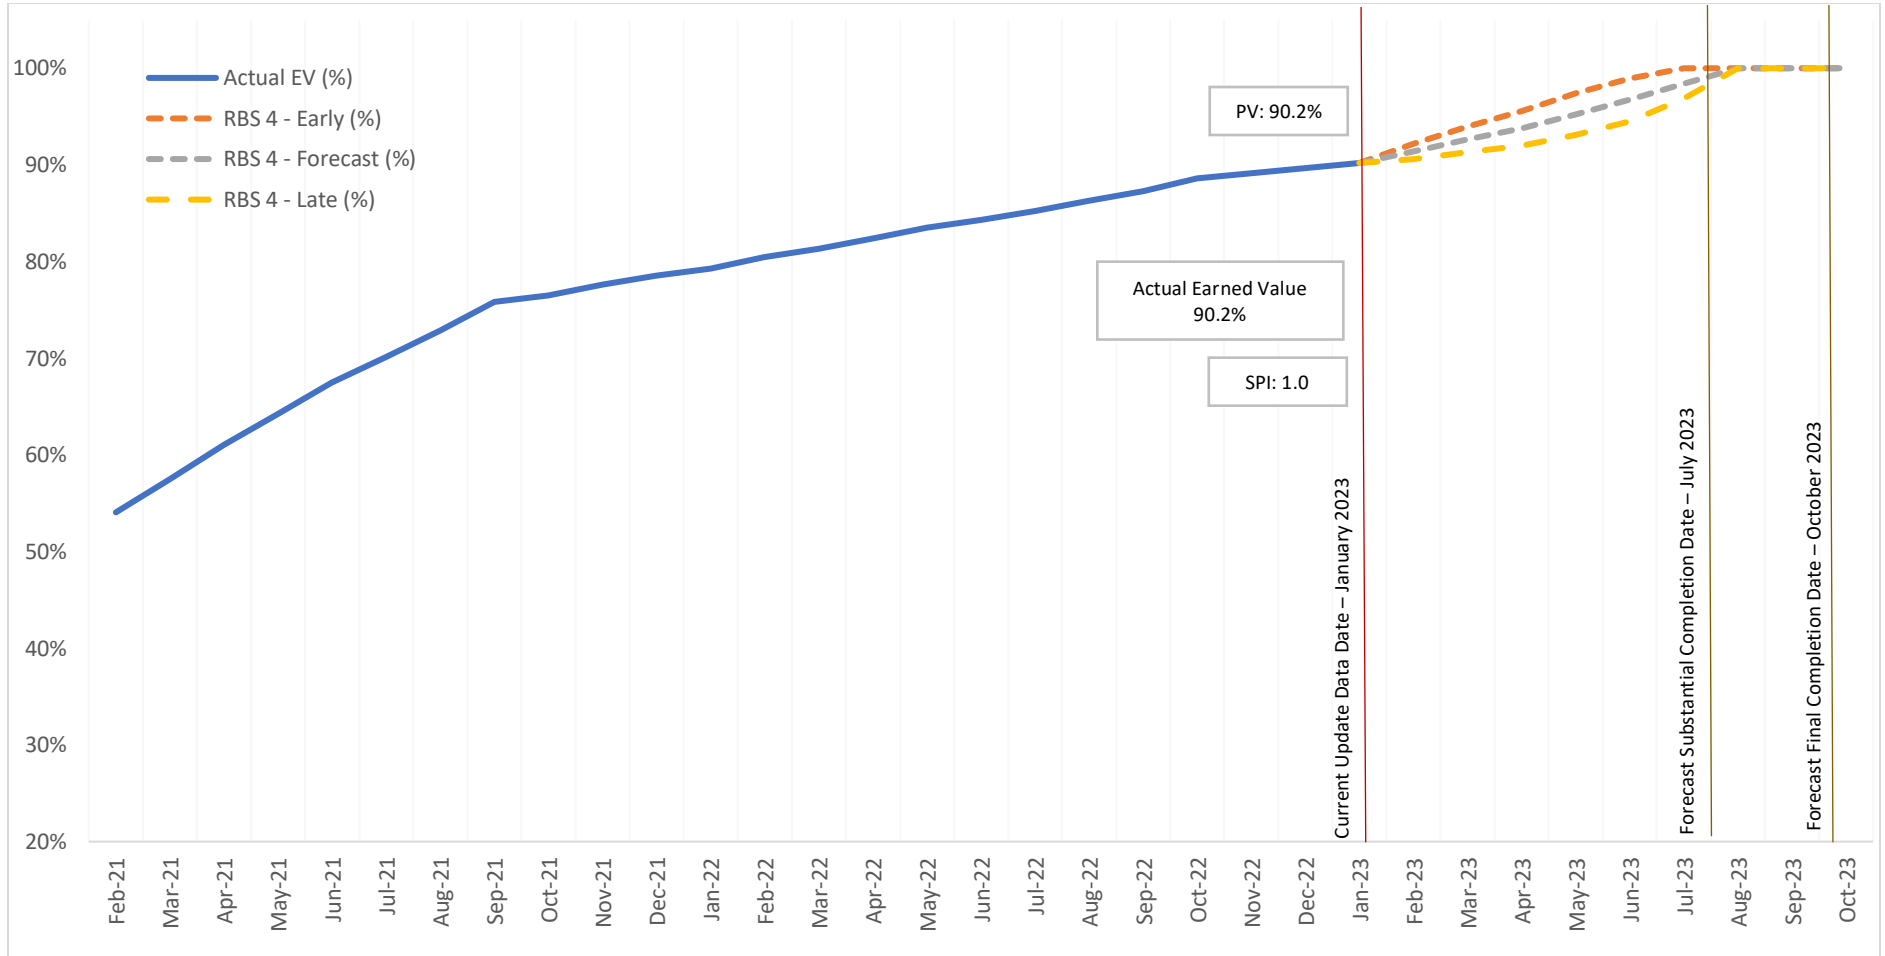


Notes:

1. The plan graphs are based on a revised forecast with a data date of February 1, 2023. The schedule finalization is under negotiation with the contractor. .
2. Earned Value represents physical progress of site activities, which is based on project team verification of site progress measurements.
3. The early dates graph is optimistic and assumes activities will take place on the schedule early dates.
4. Average graph assumes non-critical path activities are taking place mid-way of early and late dates.
5. The late dates graph assumes activities will take place on the schedule late dates. If actuals fall below late graph, it indicates schedule slippage. To provide contingency, the Schedule Performance Index (SPI) is measured against the average graph.
6. Time contingency is not included in these forecasts. This is Authority owned contingency.
7. The schedule update received shows Substantial Completion in July 2023.

CP 4 – Cost Trend

CP 4 – Cost Trend Summary (\$ Millions)

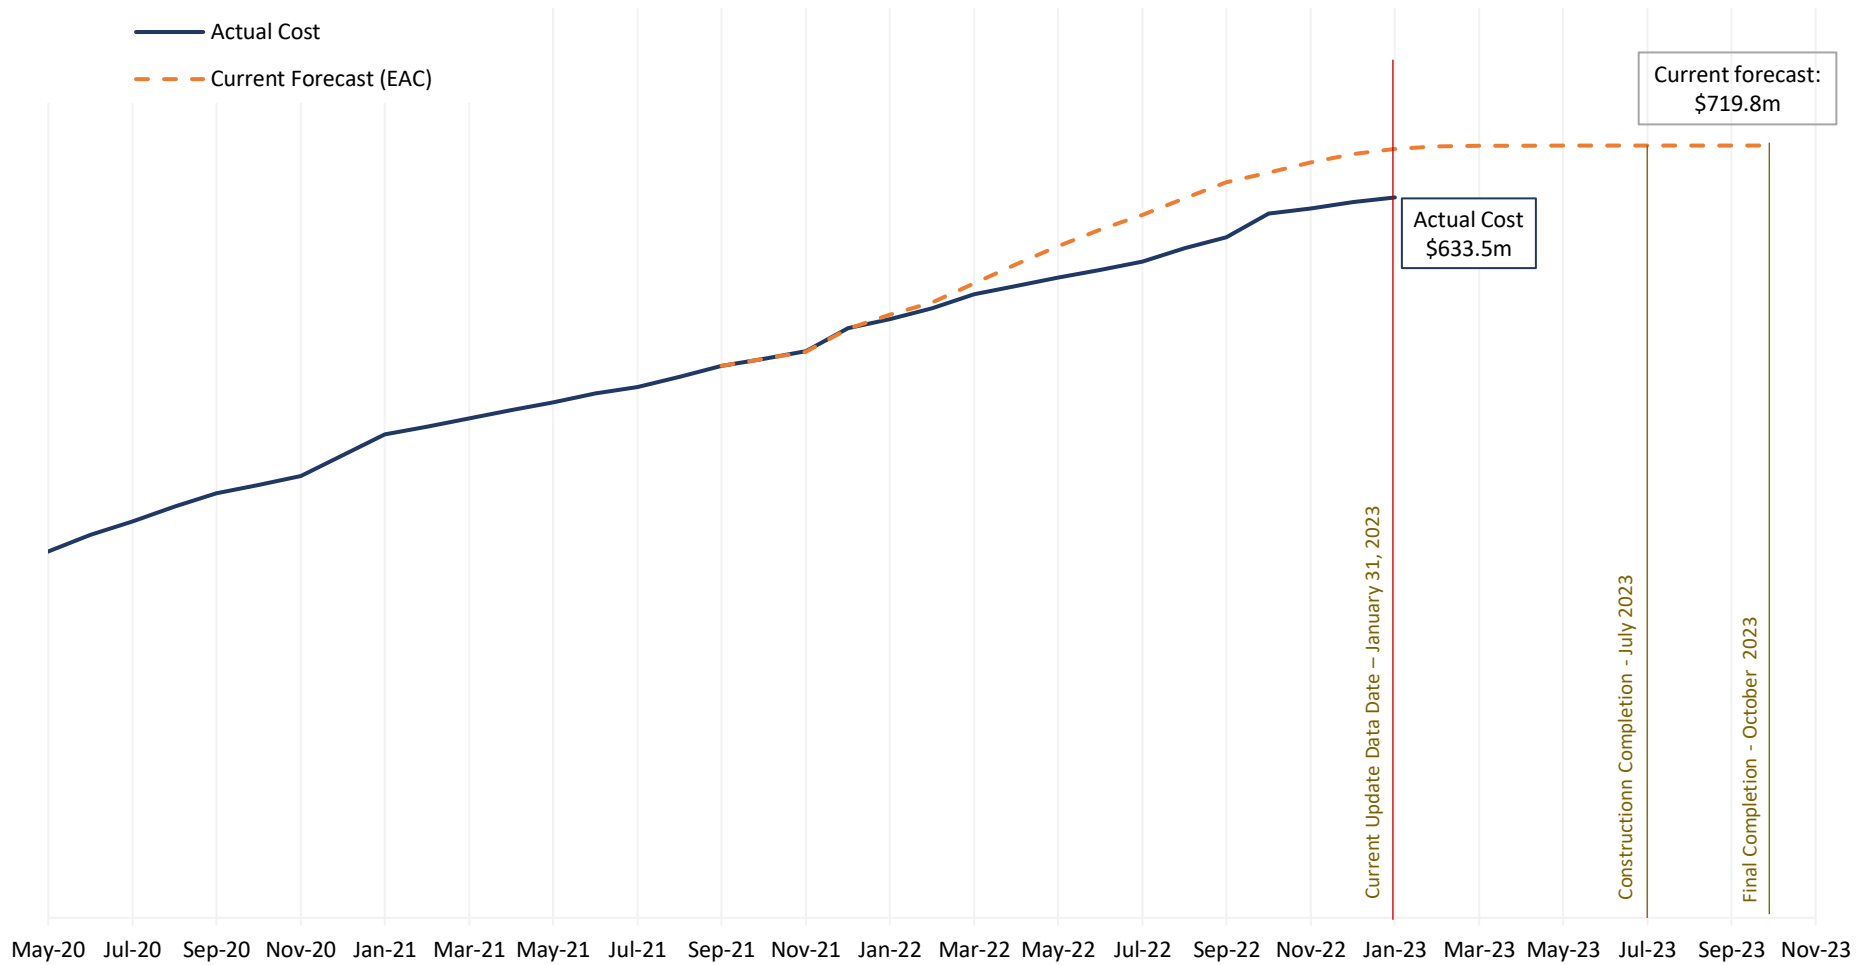


Notes:

1. The graph provides a comparison of the project actual cost performance against the current Estimate at Completion (EAC).
2. The current EAC forecast is based on the contract value and the estimated cost of expected change orders.
3. The schedule update received shows Substantial Completion in July, 2023.

CP 4 – Design-Build Expenditures

CP 4 – Monthly Expenditures (\$ Millions)

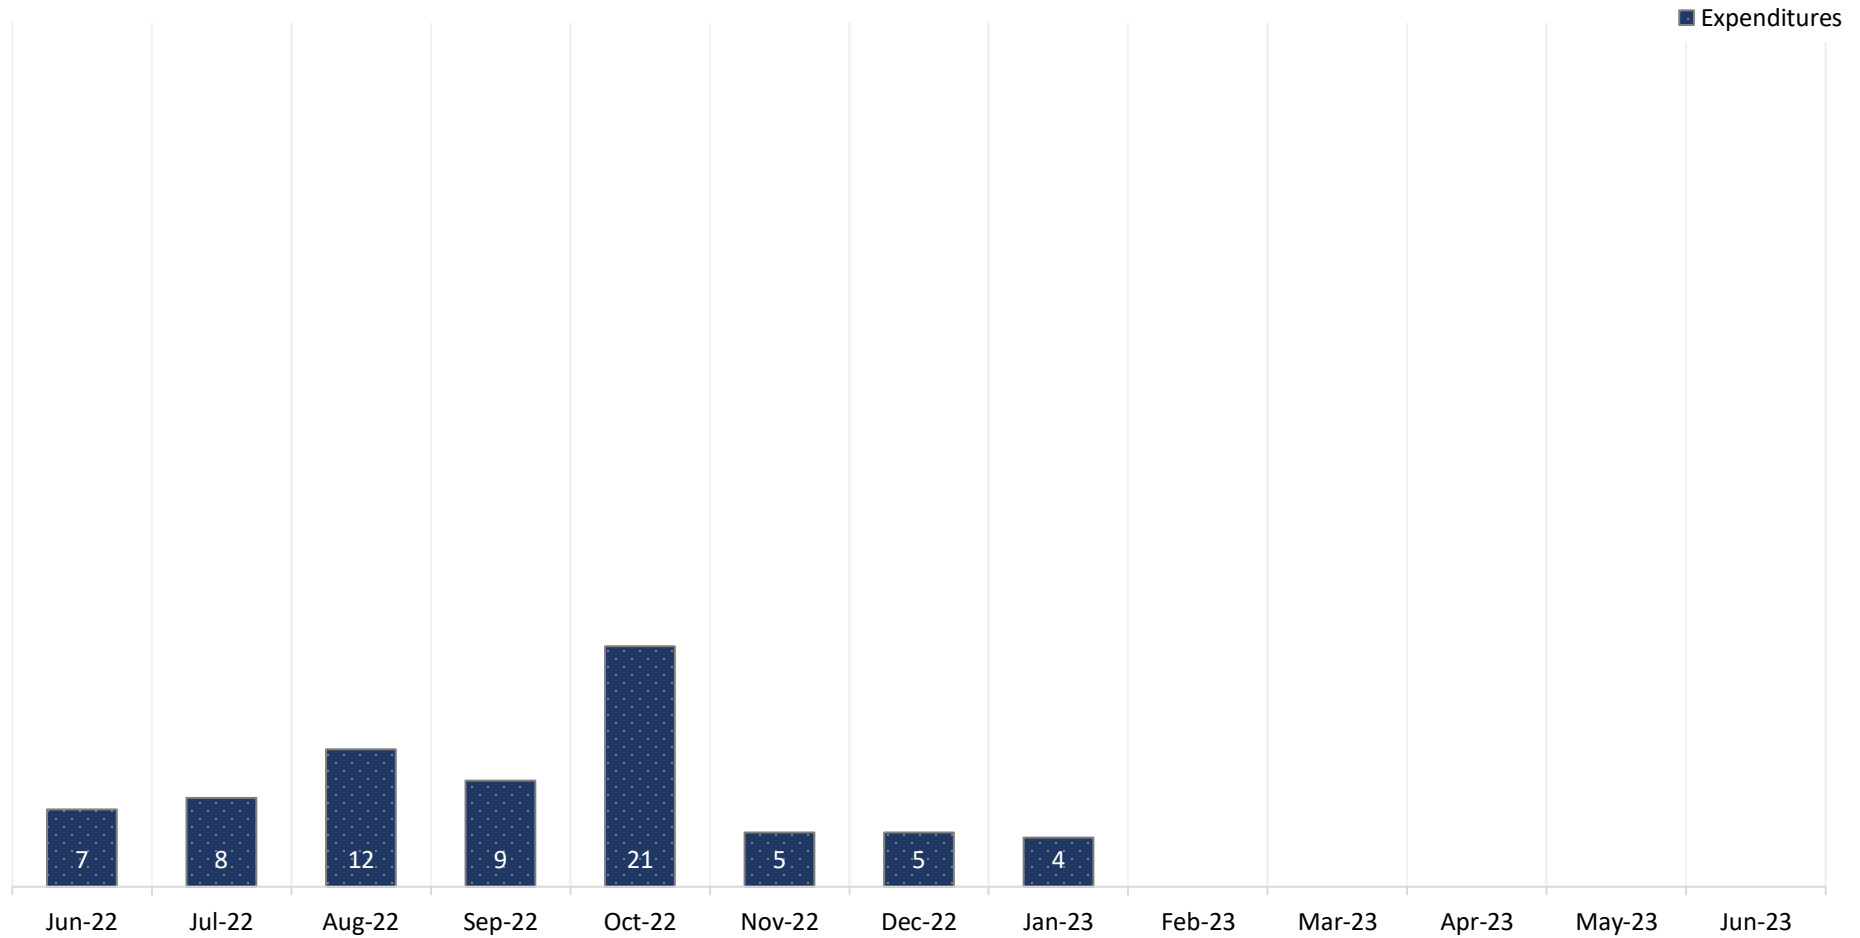

Notes:

1. Expenditures in the chart above are specific to the Design-Builder production and based on the Capital Outlay and Expenditure Report.
2. Expenditures totaled \$4.2M.
3. California Rail Builders (CRB) is unable to proceed with embankment work currently held back by completion of necessary utility relocations.


CP 4 – Change Orders (CO)

CP 4 – Change Order Status

CO Number	Title	Change Status	Amount	Executed Date
84.2	Quality Milestone Data Pack Structure and Content	Executed	\$1,669,790.98	01-20-23
170	Reimbursement of CDFW Fees	Executed	\$22,995.91	01-12-23
171	North Kern Water Storage District Additional Costs not Covered under the Contract	Executed	\$29,105.18	01-12-23
TOTAL			\$1,721,892.07	

CP 4 – Risk Contingency

CP 4 – Risk Contingency Status (\$ Millions)

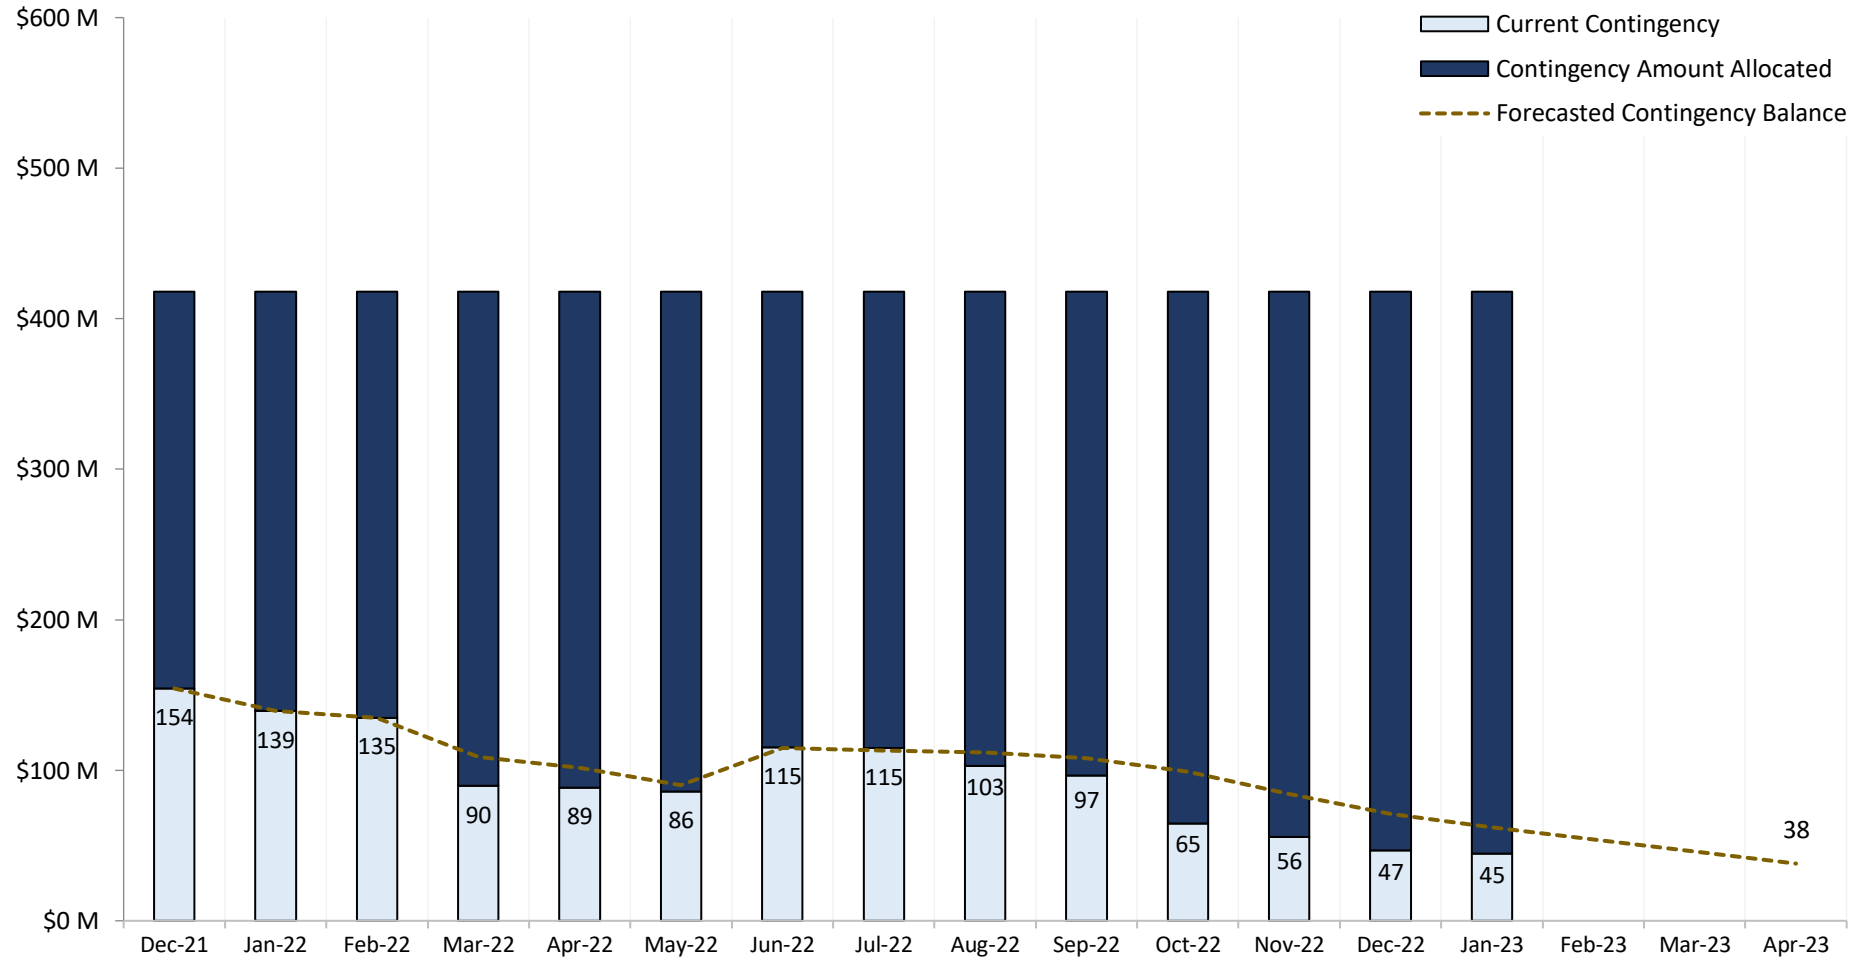


Notes:

1. Program baseline is \$418M.
2. Contingency balance updated to reflect the Board’s adoption of Resolution #HSR21-11 (Expenditure Authorization Increase).
3. Contingency Amount Allocated reflects executed change orders and Business Oversight Committee (BOC) approved items.
4. The Forecasted Contingency Balance drawdown curve is based only on agreed change orders expected to be executed within the three-month window. Due to change order negotiations and dispute resolution, timing and value of Forecasted Contingency Balance is uncertain.
5. June 2022 increases due to \$31M Business Oversight Committee approved transfer of Utility Provisional Sum from contract to contingency.

CP 4 – Monthly Construction Labor

CP 4 – Monthly Construction Workforce Total – Actual (FTE)

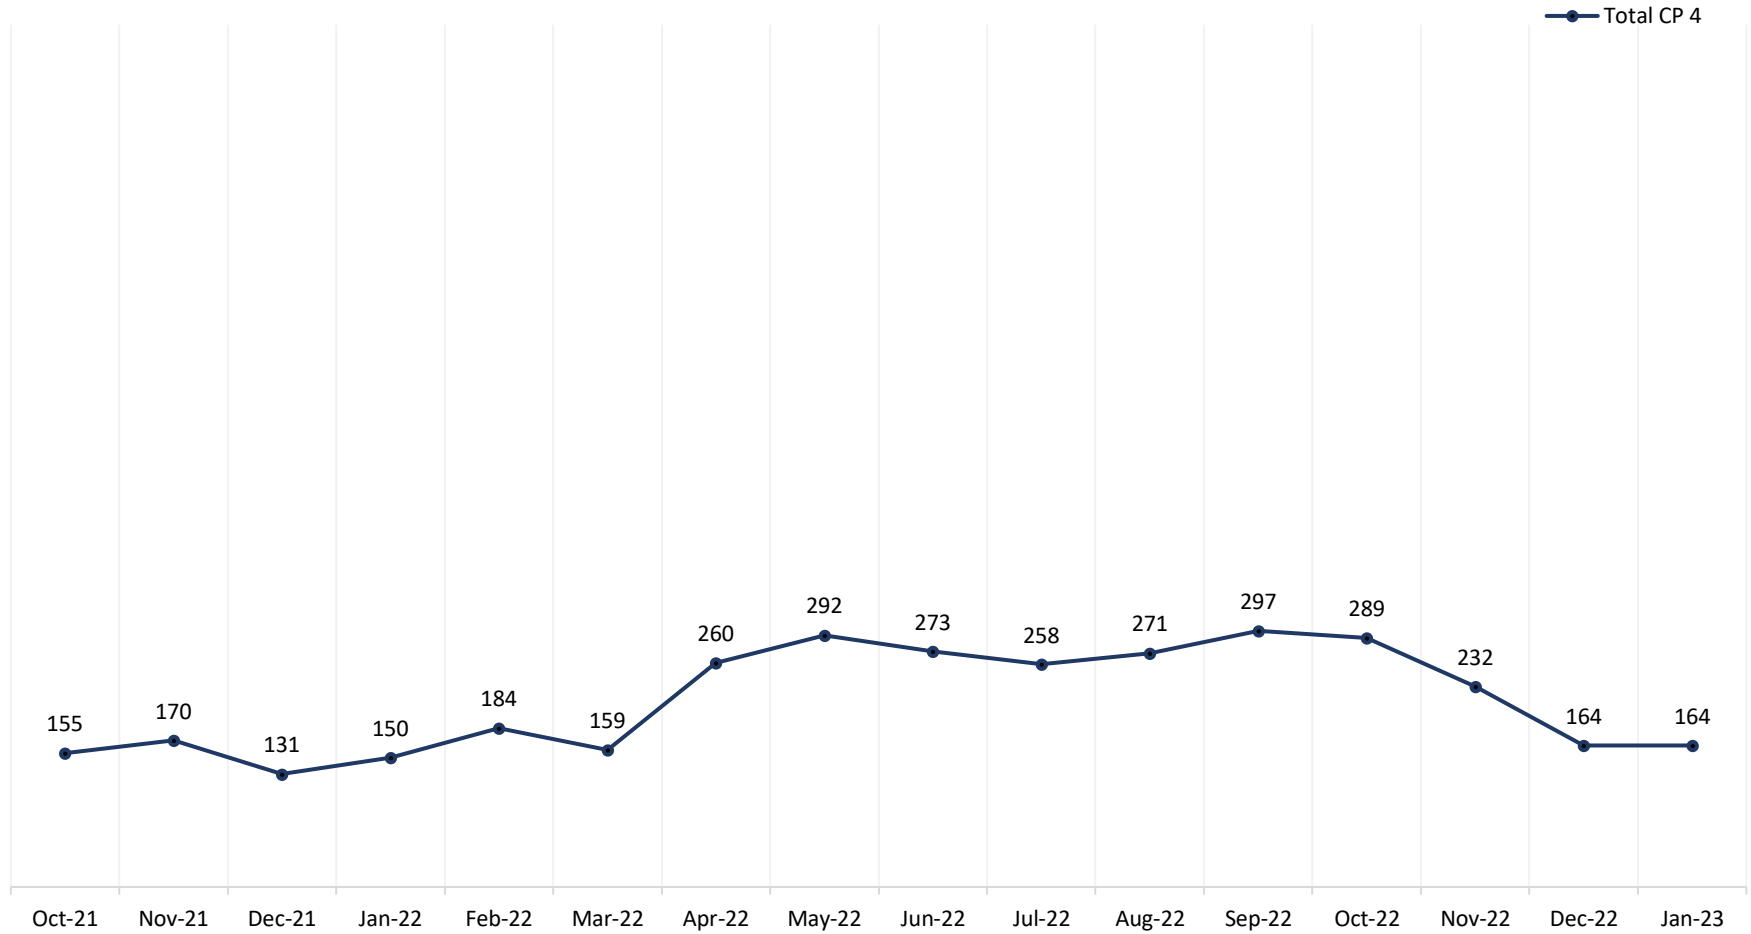


Notes:


1. The construction labor numbers (full-time employees) are based on the weekly totals divided by the number of weeks within the working calendar month and represents the Average Daily Site Workers (by week).
2. No change in the number of workers from the previous month (164).
3. Decrease in labor numbers due to multiple rain events.

CP 4 – Construction Progress

CP 4 – Construction Progress

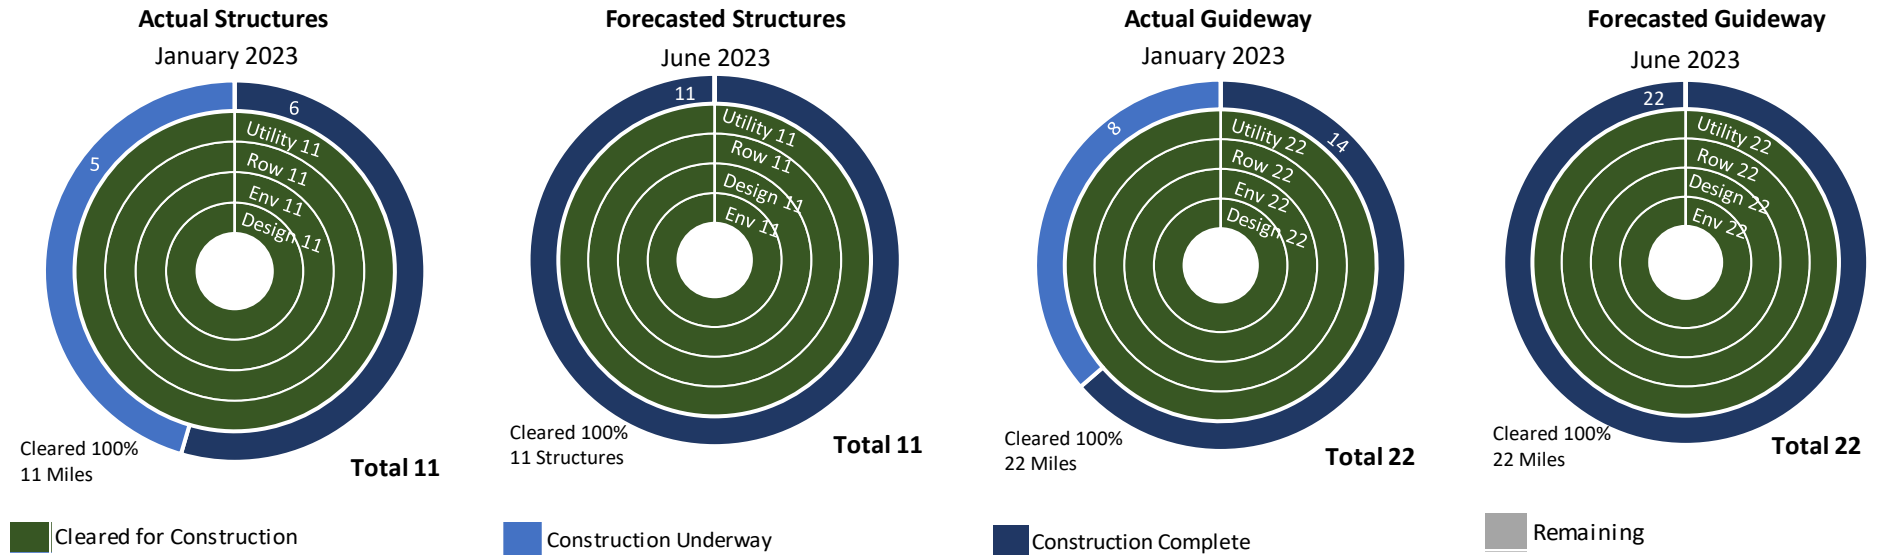

CP 4 – Structures and Guideway Progress – Forecast vs. Actual

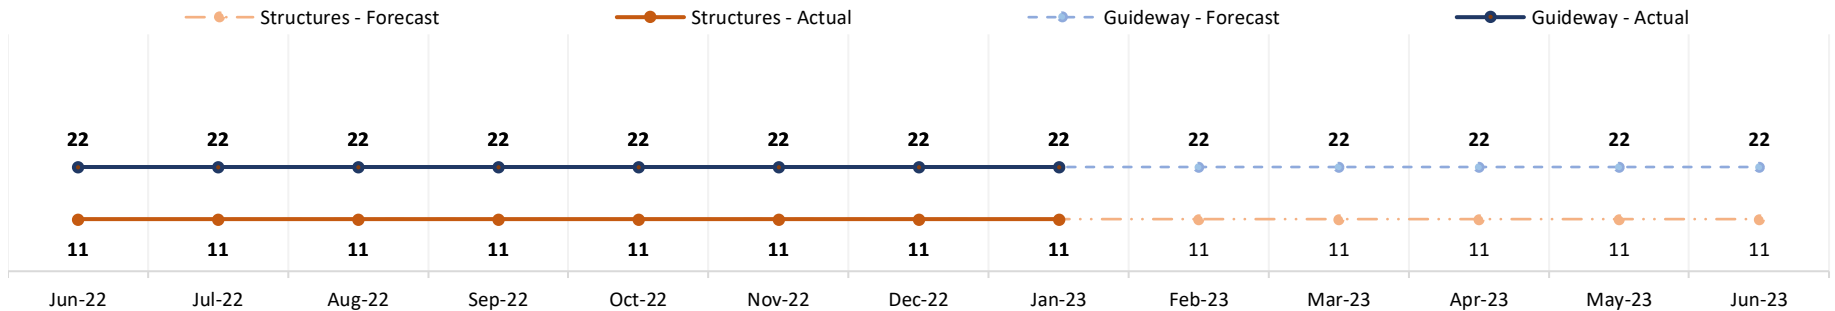

Notes:

1. The circle charts above incorporate Revised Baseline Schedules (RBS3) approved schedule.
2. Construction Complete definition:
 - a. Structure Completion – all concrete work is complete.
 - b. Guideway Completion – earthworks complete with rough grading.
3. Total Structures: 11:
 - a. 11 structures underway/construction complete.
4. Total Guideway: 22 miles. The actual miles for CP 4 are 21.5 miles but rounded to 22 miles for consistency in reporting:
 - a. 22 miles underway/construction complete.


CP 4 – Real Property/Right-of-Way (ROW)

CP 4 – Right-of-Way (ROW) Summary

Construction Package	Total Needed Parcels January 31, 2023	Total Parcels Delivered to Date January 31, 2023	Remaining Parcels to be Delivered January 31, 2023
CP 4	231	220	11

CP 4 – Parcel Delivery to Design-Builder (DB) Summary

■ Actual Delivery to DB
 ●●●● Planned Cumulative
 — Actual Cumulative

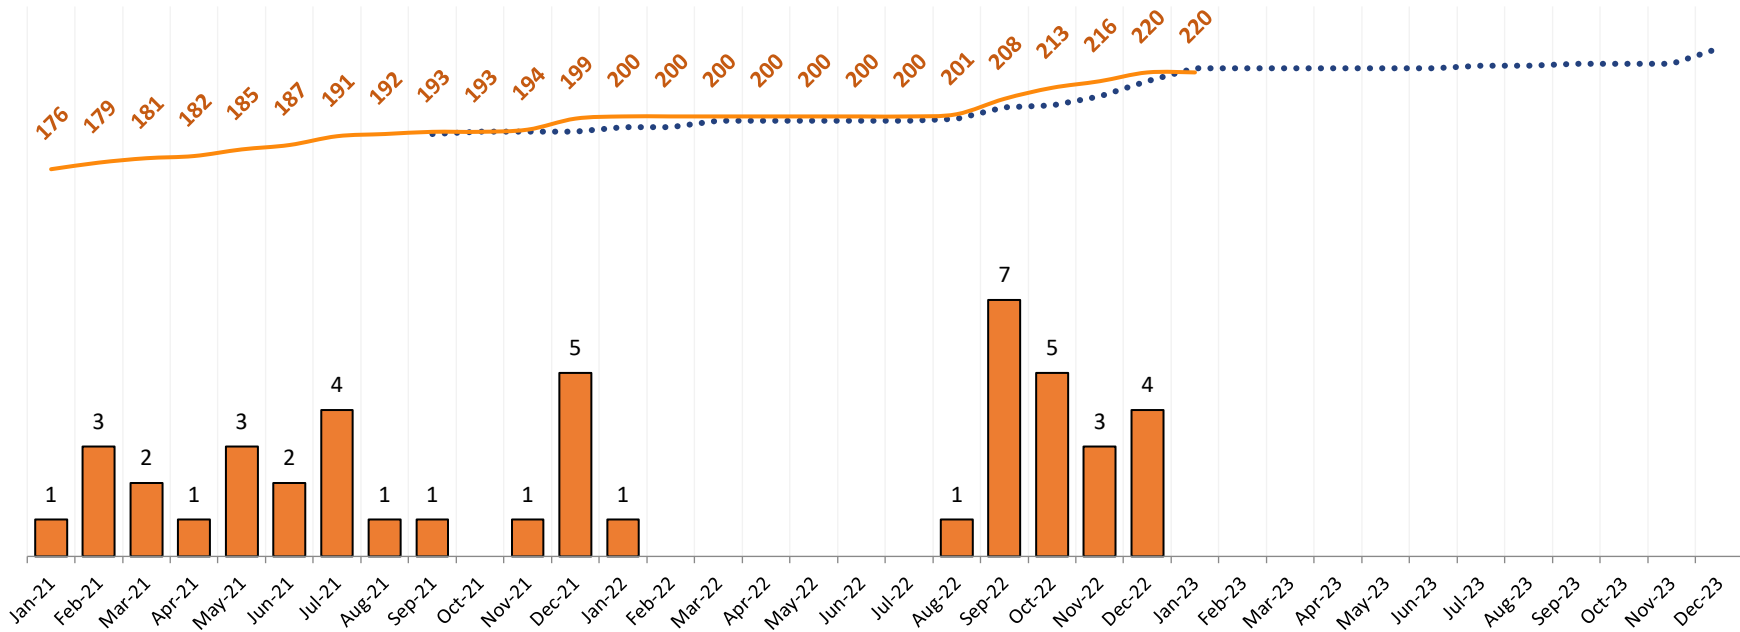

Notes:

1. This reflects the actual parcels delivered to the Design-Builder by month compared to the Revised Baseline Schedule (RBS) Revision 3.
2. Two delinquent parcels are anticipated to be delivered in February.
3. CP4 parcels planned beyond March 2023 are not required for substantial completion of construction.


CP 4 – Real Property/Right-of-Way (ROW) Railroad

CP 4 – Right-of-Way (ROW) Railroad Summary

Construction Package	Total Needed Railroad Parcels January 31, 2023	Total Railroad Parcels Delivered to Date January 31, 2023	Remaining Railroad Parcels to be Delivered January 31, 2023
CP 4	29	29	0

CP 4 – Railroad Parcel Delivery to Design-BUILDER (DB) Summary

Actual Railroad Delivery to DB
 Planned Railroad Cumulative
 Actual Railroad Cumulative

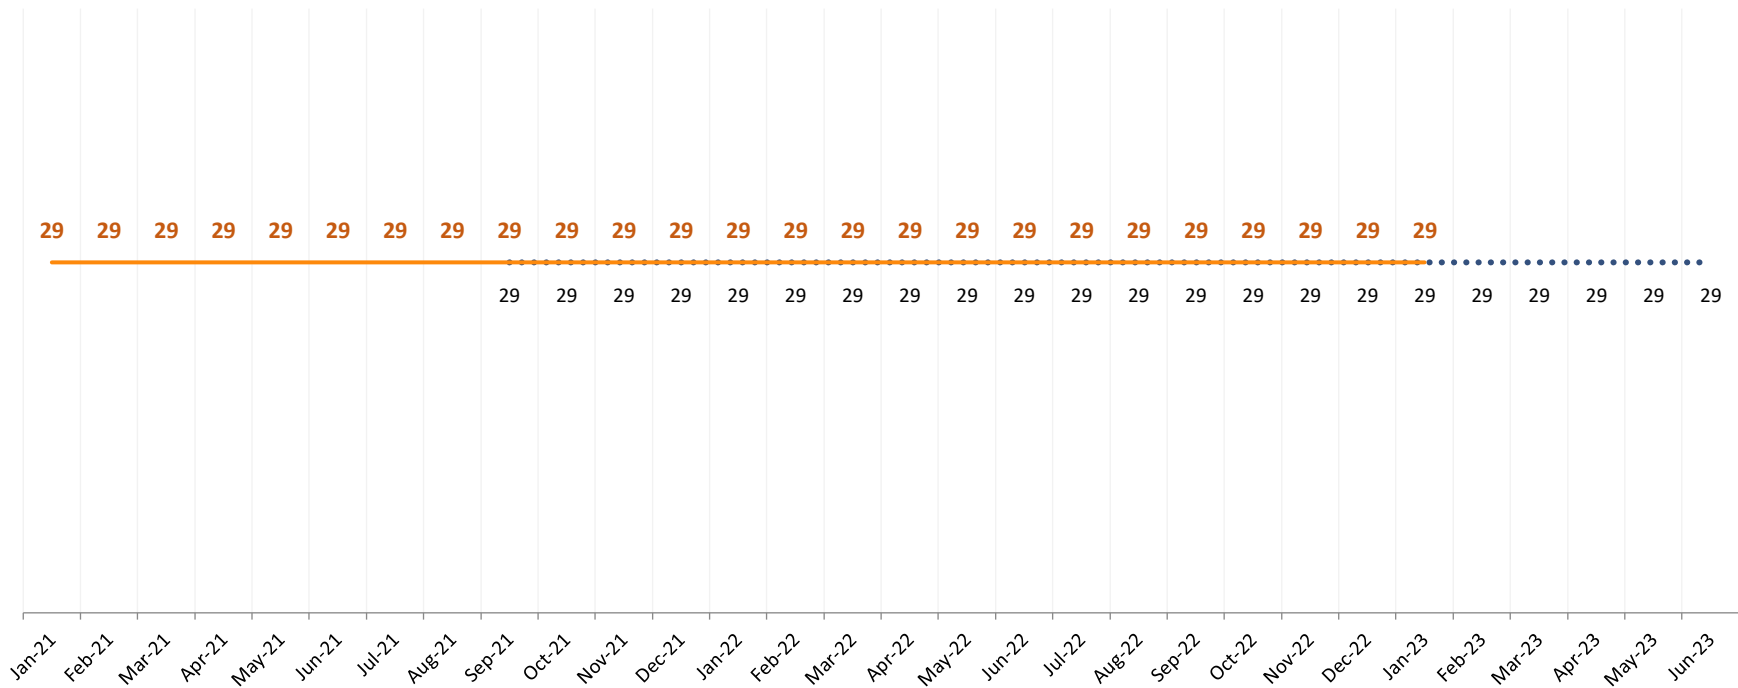


CP 4 – Tier 1 Land Right Conveyances Required Prior to Construction (PG&E, SCE, FID, FMFCD)

CP 4 – Tier 1 Land Right Conveyances Required Prior to Construction (PG&E, SCE, FID, FMFCD) Summary

Construction Package	Total Needed Land Right Conveyances January 31, 2023	Total Land Right Conveyances Approved ⁽²⁾ to Date January 31, 2023	Remaining Land Right Conveyances to be Approved January 31, 2023
CP 4	68	43	25

CP 4 – Tier 1 Land Right Conveyances Required Prior to Construction (PG&E, SCE, FID, FMFCD) Summary

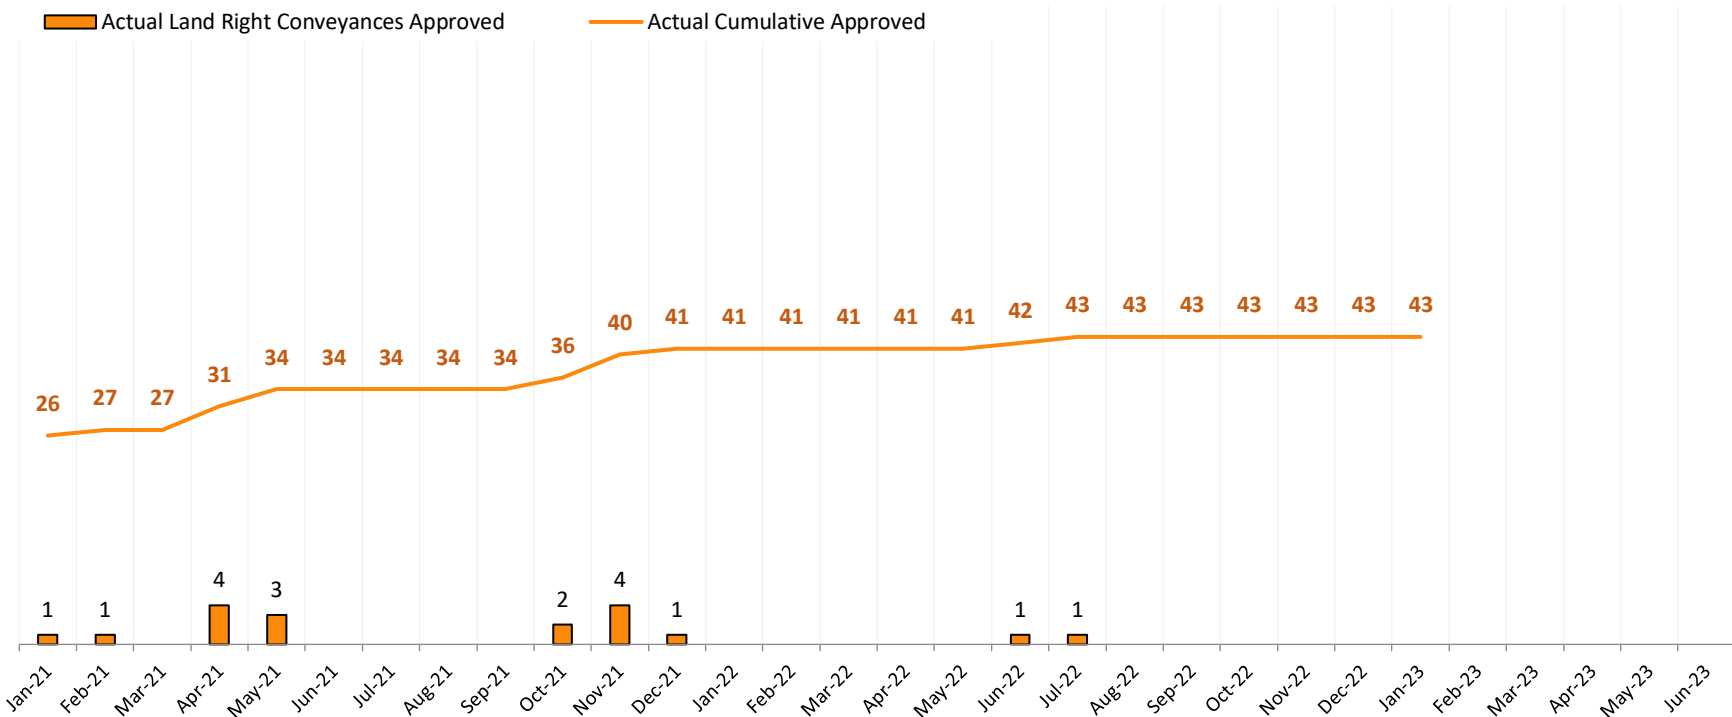

Notes:

1. The Planned Cumulative line for Land Right Conveyances is being adjusted to reflect Revised Baseline Schedule (RBS) Revision 3 and will be reflected in a subsequent report.
2. The term "Approved" is defined as land right conveyances with Director of Real Property for signature, PG&E for signature, or recorded.

Project Development Schedule (Environmental Clearance) – Record of Decision (ROD)

Project Development Schedule (to ROD)

Number	Segment	Progress	Complete Purpose and Need Statement		Complete Alternatives Analysis		Board Concurrence of Preliminary Preferred Alt. Draft EIR/EIS		Publish Draft EIR/EIS		Publish Final EIS and Obtain ROD		Date EIR/EIS To Be Completed	
			Last Month	Current	Last Month	Current	Last Month	Current	Last Month	Current	Last Month	Current	Last Month	Current
Document Complete	Merced to Fresno	Plan Forecast % Complete	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%
Document Complete	Fresno to Bakersfield	Plan Forecast % Complete	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%
Document Complete	CV Electrical Interconnections	Plan Forecast % Complete	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%
Document Complete	Locally Generated Alternative (F-B)	Plan Forecast % Complete	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%
Document Complete	Central Valley Wye (M-F)	Plan Forecast % Complete	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%
Document Complete	Bakersfield to Palmdale	Plan Forecast % Complete	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%
Document Complete	Burbank to Los Angeles	Plan Forecast % Complete	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%
Document Complete	San Jose to Merced	Plan Forecast % Complete	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%
Document Complete	San Francisco to San Jose	Plan Forecast % Complete	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%
1	Los Angeles to Anaheim	Plan Forecast % Complete	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	May-23 Jul-23 ¹ 89%	May-23 Aug-23 ¹ 90%	Jun-24 Aug-24 ¹ 0%	Jun-24 Sep-24 ¹ 0%	Aug-24 ¹	Sep-24 ¹
2	Palmdale to Burbank	Plan Forecast % Complete	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Aug-22 Sep-22 100%	Aug-22 Sep-22 ² 100%	Sep-23 Nov-23 0%	Sep-23 Nov-23 8%	Nov-23	Nov-23
3	Heavy Maintenance Facility (HMF)	Plan Forecast % Complete	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Complete Complete 100%	Apr-16 TBD 0%	Apr-16 TBD 0%	Sep-16 TBD 0%	Sep-16 TBD 0%	Feb-21 TBD 0%	Feb-21 TBD 0%	TBD	TBD

- Notes:**
- For the Los Angeles to Anaheim project section, an information item is planned for discussion at the March 2023 PDC meeting regarding future schedule adjustments, pertaining to potential changes to the project description. Those schedule adjustments will be brought back to the PDC later this year for review and approval.
 - The Palmdale to Burbank Draft EIR/EIS was released to the public on September 2, 2022. On September 20, 2022, the Authority extended the public comment period from 60 days to 90 days. The public comment period closed on December 1, 2022.

Project Development – Key Actions

Project Development (Environmental Clearance) – Key Actions Summary

Project Section	Key Actions
San Francisco to San Jose	Environmental Clearance activities complete. The Rail Development Partners (RDP) is supporting the Authority litigation activities.
San Jose to Merced	Environmental Clearance activities complete. The RDP is participating in post-ROD coordination with external stakeholders such as the Transportation Authority of Monterey County, Grasslands Water District, City of San Jose, and others.
Central Valley Wye	Conducted monthly progress meeting with County of Madera on Fairmead mitigation projects. Environmental Clearance activities complete. Transition to Merced Extension (Merced to Madera).
Locally Generated Alternative	Environmental Clearance activities complete. Transition to Bakersfield Extension (LGA).
Bakersfield to Palmdale	Work through Notice of Determination/Record of Decision (NOD/ROD) has been completed. The Authority has continued to meet with key stakeholders (e.g., Center for Biological Diversity, City of Palmdale) as necessary.
Palmdale to Burbank	The Draft EIR/EIS was released to the public on September 2, 2022. The public comment period was extended from 60 days to 90 days and closed on December 1, 2022. Continued to coordinate with the Regional Consultants to prepare responses to comments received on the Draft EIR/EIS.
Burbank to Los Angeles	Work through NOD/ROD has been completed. Project closeout activities are ongoing.
Los Angeles to Anaheim	Continued integrating additional revised environmental deliverables from Burlington Northern Santa Fe Corporation (BNSF) pertaining to the Colton and Lenwood project components into the assembled Administrative Draft EIR/EIS. An information item is planned for discussion at the March 2023 PDC meeting regarding future schedule adjustments for the LA-A project section, pertaining to potential changes to the project description. Those schedule adjustments will be brought back to the PDC later this year for review and approval.

Project Development (Post-ROD) – Key Actions Summary

Project Section	Key Actions
Merced Extension (Merced to Madera)	Stantec Inc. under agreement HSR 22-02, continues to make progress on the early actions of this Project, including submittal of various Draft documents such as the Project Management Plan-Draft.
Fresno to Bakersfield Locally Generated Alternative (LGA)	The HNTB Corporation (HNTB), under agreement HSR 22-01, continues to make progress on the early actions of this Project, including submittal of various Draft documents such as the Project Management Plan and the BNSF Shoofly Alignment - Draft.
